



EAST AFRICAN  
CRUDE OIL  
PIPELINE

MONTHLY

# NEWSLETTER

EACOP TZ

ISSUE 8  
April 2024



## EACOP Honored for Local Content Achievement

- Construction
- Land and Social
- Human Rights
- Regulatory and Compliance

# CONTENTS

## 03 INTRODUCTION

## 04 CONSTRUCTION

## 06 EACOP WINS RECOGNITION FOR LOCAL CONTENT EXCELLENCE

## 07 LAND & SOCIAL

### LAND ACQUISITION UPDATES ..... 7

Additional Land Acquisition at Mcpy12, Access Road and Re-Route at Kp961 ..... 7

Compensation Agreements Signing ..... 8

Supplementary Valuations ..... 8

Transitional Support Services ..... 9

Grave Removal Progress ..... 10

### LIVELIHOOD RESTORATION ..... 12

Livelihoods Restoration Program (LRP) ..... 12

LRA 1 - 3: Sustainable Agriculture ..... 12

Implementation progress for LRA1 - 3 on Conservation Agriculture ..... 12

Benefits of the Sustainable Agriculture..... 12

### REPLACEMENT HOUSING ..... 14

#### STAKEHOLDER ENGAGEMENT – GOVERNMENT

#### AND COMMUNITY ..... 15

High-level Engagement and support ..... 15

Community Safety ..... 16

Engagement Progress ..... 18

Vulnerable Ethnic Groups Self-Identifying as Indigenous

People Engagements ..... 18

Community Level Engagement..... 19

Government & Regional Engagement ..... 19

Grievance Management ..... 20

Gender Action Plan..... 20

### PROJECT INDUCED IN-MIGRATION (PIIM) ..... 20

### IMAGERY ACQUISITION ..... 21

## 23 REGULATORY COMPLIANCE

Permitting in Tanzania ..... 23

Regulatory Compliance and Assurance..... 25



# INTRODUCTION

East African Crude Oil Pipeline (EACOP) Ltd, is a special purpose company, that will construct and operate the East African Crude Oil Pipeline (EACOP), a 1,443km long crude oil export pipeline that will transport Uganda’s oil from Kabaale- Hoima in Uganda to the Chongoleani Peninsula near Tanga Port in Tanzania for export to the international market.

This major export system, 296km in Uganda and 1,147KM in Tanzania, with a transportation capacity of 216,000bopd comprises of a 24 inch, insulated, heat traced and buried pipeline, six pumping stations (2 in Uganda and 4 in Tanzania), two pressure reduction stations and a Marine Storage Terminal.


The Company is operated by its Shareholders Agreement in which Total Energies (62%), Uganda National Oil Company (UNOC - 15%), Tanzania Petroleum Development Corporation (TPDC - 15%) and CNOOC (8%) are shareholders.

This update aims to provide the eight Authorities in Tanzania, 27 Districts/ Towns/ City Councils hosting the EACOP project with a status report on ongoing activities in their areas. The goal is to convey practical information about the current field activities, facilitating engagement and keeping the authorities informed.



## EAST AFRICAN CRUDE OIL PIPELINE (EACOP) PROJECT TANZANIA – APRIL UPDATE


### Pipeline Route

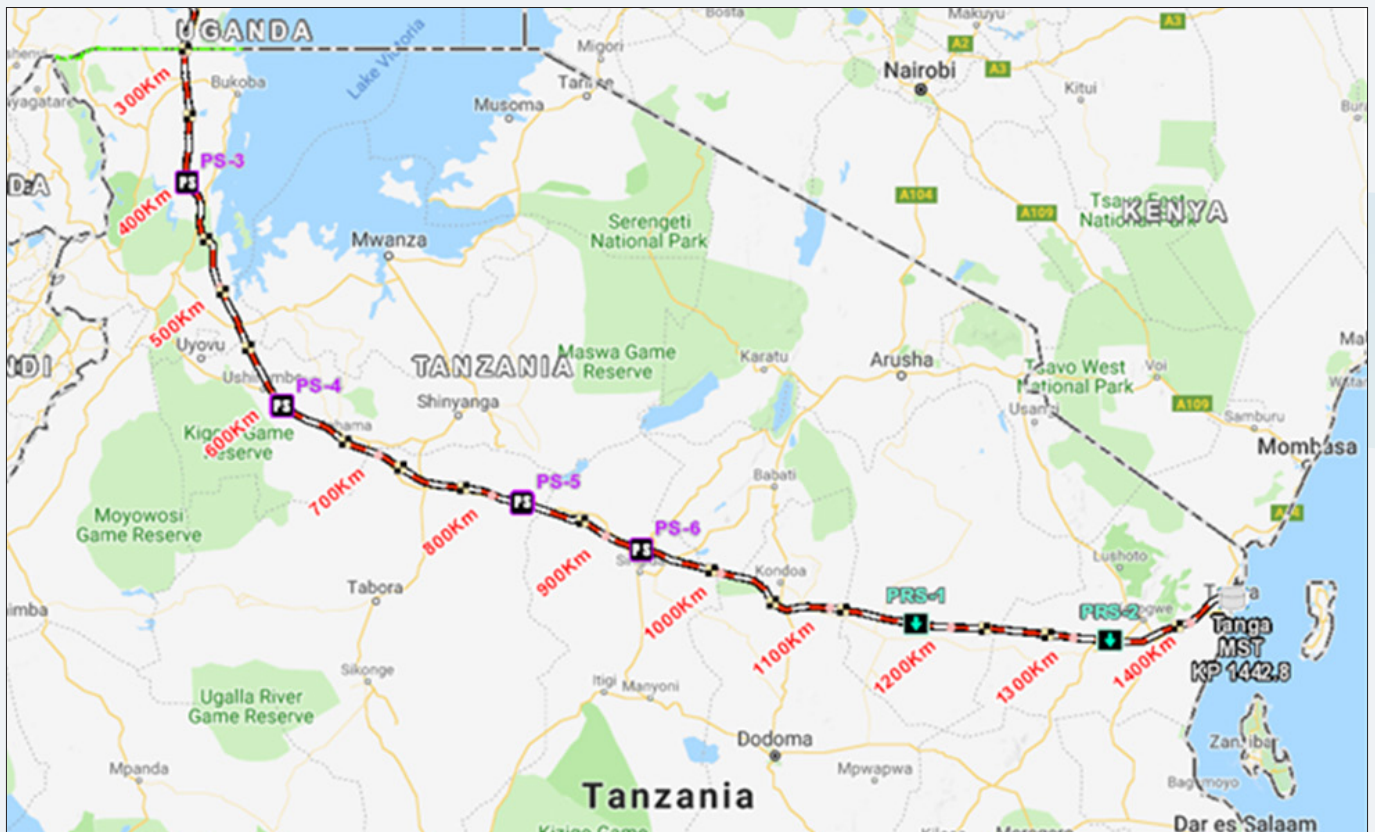

Location of EACOP pipeline route and permanent Above Ground Installations (AGIs) (PS: Pump Stations, PRS: Pressure Reduction Stations, MST: Marine Storage Terminal)

# PROJECT CONSTRUCTION

## Project progress highlights as of April 2024

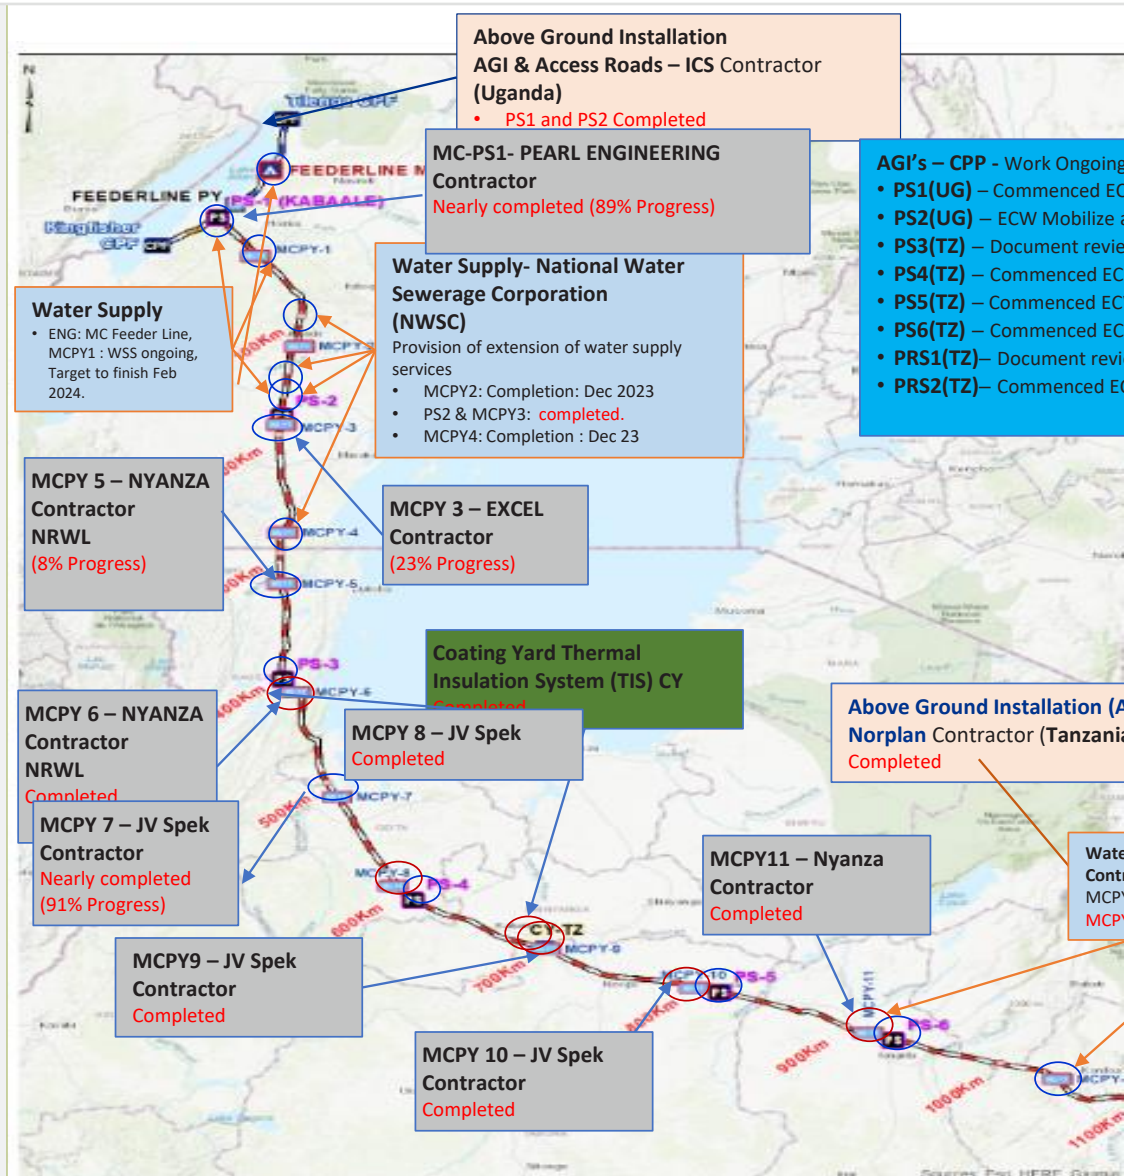

### Pipeline, Main Camps and Pipe Yards (MCPY)

- CPP Pipeline Crossings Geotechnical Survey ongoing.
- CPP Pipeline Crossings Topographical Survey completed.
- Nyanza Roads Limited is proceeding with MCPY-05 Early Civil Works.
- JV Spek finalizing MCPY-16 Early Civil Works, 1 zone handed over to CPP for camp preparation.
- CPP (and sub-contractors) constructing camps at MCPY-06, MCPY-08, MCPY-10, MCPY-11 and MCPY-15. Mobilization commenced for MCPY-13 and MCPY-14.
- CPP equipment and materials storage at MCPY-09.
- Kagongwa Road finalizing with Road Signs installations.
- Pipe deliveries from Dar es Salaam port to the TIS continue.

### Above Ground Installation (AGI): Pump Stations (PS) & Pressure Reduction Stations (PRS)


- CPP proceeding with cut and fill works at PS-3, PS-5 (Igunga), PS-6 (SIngida), PRS-1 and PRS-2 (Handeni).
- CPP finalizing PS-4 (Bukombe) Topsoil Removal. Backfilling at the Power Generator area has begun.
- CPP proceeding with PS-3 access road clearing, TARURA road upgrade has been completed.

### Thermal Insulation System (TIS) - the Coating Yard facility

- TIS plant inauguration event was held on 26th March.
- Continued delivery of pipe sections to the TIS in readiness for initial pipe coating.

### Marine Terminal & Tanks (MTT)

- DOCG has completed concrete pouring at Re-circulation heat exchangers footing and pedestal (with anchor bolts), concrete curing ongoing.

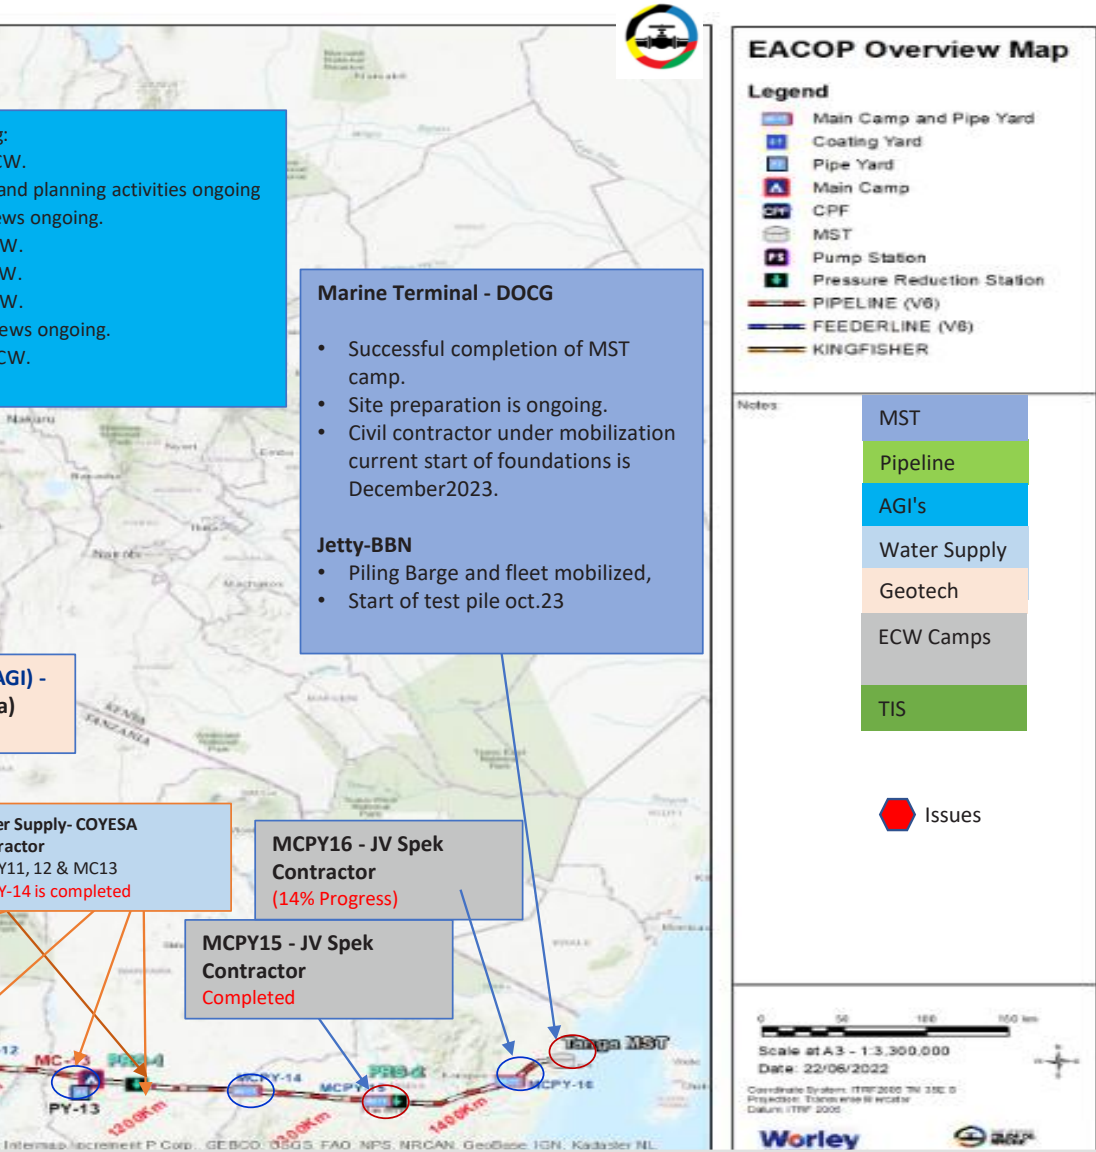

and planning activities ongoing  
works ongoing.

**Marine Terminal - DOCG**

- Successful completion of MST camp.
- Site preparation is ongoing.
- Civil contractor under mobilization current start of foundations is December 2023.

**Jetty-BBN**

- Piling Barge and fleet mobilized,
- Start of test pile oct.23

er Supply- COYESA  
ractor  
Y11, 12 & MC13  
Y-14 is completed

**MCPY16 - JV Spek Contractor**  
(14% Progress)

**MCPY15 - JV Spek Contractor**  
Completed

- DOCG has engaged a Subcontractor for a Site Batching Plant, currently proceeding with foundation works.
- DOCG has completed concrete pouring for Ring Beam of Tank A, Tank B Ring Beam concrete pouring has commenced. Levelling works ongoing at Tanks C and D.
- DOCG continues routine engagements with all Chongoleani peninsula communities.

**Jetty**

- BBN continues precast elements installations at load out facility (LOF) and offshore concrete pouring activities.
- BBN completed piling operations at LOF.
- BBN is currently installing pile plug reinforcement bars into piles.

- Stakeholder engagement continues with the communities of Chongoleani peninsula on BBN jetty construction activities as well as engaging other marine operators and stakeholders with a presence near or traversing close to the BBN operations.

EACOP Project Social team continues to observe and guide all Contractor stakeholder engagement activities in Project Affected Communities including the recruitment of unskilled and semi-skilled workers from the communities most local to the work.

EACOP Cultural Heritage Monitors continue to observe all ground disturbance activities at Marine Terminal and Tanks (DOCG), PS-3 Access Road, PS-4, PS-5, PS-6, PRS-1 and PRS-2 (all CPP).

# EACOP WINS RECOGNITION FOR LOCAL CONTENT EXCELLENCE

In line with Local Content Vision EACOP achieved another key milestone in local content implementation in Tanzania: as the first winner among the companies executing strategic projects that implement local content well.

The recognition was made by National Economic Empowerment Council of Tanzania [NEEC] in their 4th National Local Content Forum on 28 April 2024. NEEC is under Prime Minister office with role of coordinating local content initiatives and monitoring implementation at the National level.

Since the inception of the project local content initiatives has been geared toward; upskilling Tanzanians through training, internship, scholarship, train the trainer program, collaboration with education institutions to enhance their capacity, and building local vendors capacity through industry enhancement centre (IEC) program.





# LAND & SOCIAL

## LAND ACQUISITION UPDATES

### Additional Land Acquisition at Mcpy12, Access Road and Re-Route at Kp961:

Entitlement Briefing for all 26 PAPs at MCPY12 and KP961 has been successfully completed. Compensation Agreement signing will take place after a 14-day reflection period, which is expected to be around the third week of May 2024.



Photo: Entitlement Briefing session at MCPY12, Serya Mtaa, Kondoa District

## Compensation Agreements Signing

The number of unsigned PAPs stands at 79. Two more PAPs expect to sign compensation agreements by mid-May 2024. These are among the PAPs whose claims were approved for Entitlement briefing and compensation agreement signing during escrow review of 20th March 2024. Ongoing due diligence for other 6 unsigned claims.

Progressing with the field mission for searching the unsigned PAPs.

**Table: Status; unsigned compensation agreements**

Summary: Eacop Project - Unsigned Compensation Agreements as Of 30 April 2024									
Unsigned CA categories (reasons)	Regions								
	Kagera	Geita	Shinyanga	Tabora	Singida	Dodoma	Manyara	Tanga	Total
<b>Absent PAPs</b>	8	3	3	0	0	0	5	2	21
<b>Unknown PAPs</b>	0	9	4	3	0	1	1	0	18
<b>Incomplete inheritance process</b>	0	0	0	0	0	0	0	2	2
<b>Disputes over the ownership of land and/or assets</b>	3	0	2	4	8	4	0	12	33
<b>Refusal (unhappy with the compensation amount)</b>	0	0	1	0	1	0	0	1	3
<b>Grievance (Unresolved grievance at the end of NTV - required supplementary valuation)</b>	0	0	0	0	0	1	0	0	1
<b>Under liquidation process</b>	0	0	0	0	0	0	0	1	1
<b>Total Unsigned Compensation Agreements (CAs)</b>	<b>11</b>	<b>12</b>	<b>10</b>	<b>7</b>	<b>9</b>	<b>6</b>	<b>6</b>	<b>18</b>	<b>79</b>

## Supplementary Valuations

The team has mobilized to the field to sign compensation agreements for three recently approved supplementary valuations, primarily for newly identified graves. One out of the three compensation agreements have been signed. The Entitlement Briefing and Compensation Agreement (EBCA) Team is in progress with signing the remaining agreements, aiming to complete them by the second week of May 2024.



## Transitional Support Services

99% of eligible PAHs have received April transitional support deliveries. These include actual food baskets and cash transfers. **Categories of support differ from zone to zone depending on the calendar of distribution as shown below:**

**Zone One (1) regions (Kagera, Geita and Shinyanga).** Highly impacted PAHs have received food baskets deliveries. No cash transfers were made since the Transitional Support services for Partially impacted PAHs was completed in March 2024.

**Zone Two (2) regions (Tabora, Singida, Dodoma and Manyara),** All eligible PAHs received cash transfers. Transitional Support Services for Partially Impacted PAHs ends in April 2024. Support for Highly impacted PAHs will proceed until October 2024.

**Zone Three (3) region (Tanga),** Highly impacted PAHs have received actual food baskets and partially Impacted PAHs received cash transfers. Support for Partially impacted PAHs ends in April 2024. Support for Highly impacted PAHs will proceed until October 2024.

**Overall progress:** Seven rounds of Transitional support services have been successfully delivered to eligible Project Affected Households in the Pipeline, MST terrestrial and diver fishers.

The transitional support services programme has been completed for all partially impacted PAHs eligible for six months support. Ongoing transitional support deliveries for Highly impacted PAHs eligible for twelve months support.



### PPL TSS metrics for April 2024 are reflected below

Transitional Support Deliveries – April 2024						
S/N	Region	# PAPs	Actual food baskets	Cash transfers	Total	%
1	Kagera	170	169	0	169	99%
2	Geita	120	120	0	120	100%
3	Shinyanga	42	42	0	42	100%
4	Tabora	843	0	836	836	99%
5	Singida	1,159	3	1,144	1,147	99%
6	Dodoma	765	2	755	757	99%
7	Manyara	418	0	418	418	100%
8	Tanga	1,334	502	813	1,315	99%
<b>Total</b>		<b>4,851</b>	<b>838</b>	<b>3,966</b>	<b>4,804</b>	<b>99%</b>



Food basket distribution in April 2024.

## Grave Removal Progress

1,120/1,123 of the original Pipeline graves have been completed removed from the Project land.

One (1) new grave has been identified in the Pipeline Right of Way. This makes a total of 15 newly identified graves and a total of 18 unremoved graves. Preparation of valuation report for the newly identified grave ongoing.

Completed EBCA signing for 12/15 newly identified graves.



1,120  
**Graves have  
been completed**

Application for grave removal notice was made, follow-up with Ministry of Land and TPDC on status of gazettelement of the Notice ongoing, risk of impact if not removed prior to start of pipeline construction.

## Statistics: Pipeline unremoved graves

Original graves list					
S/N	Region	District	Village	No of Graves	Status
1	Geita	Geita	Igando	1	Ritual performance was delayed due to the absence of other family members in the day of grave removal exercise. Ritual performance already performed, plan for removal of the grave underway.
2	Kagera	Muleba	Nyakanyasi	1	EBCA signing completed in March 2024. Plans for the removal of the grave are ongoing.
3	Singida	Iramba	Ng'Anguli	1	Family land dispute over ownership of the impacted assets (including graves). The land dispute is in the High Court
<b>Total</b>				<b>3</b>	

## Newly identified Graves

S/N	Region	District	Village	No of Graves	Status
1	Singida	Singida DC	Idisimba	4	Compensation agreement signing completed in March 2024. Graves removals Notice to be issued prior to planning for removal
2	Singida	Mkalama	Tumuli	3	Compensation agreement signing was completed in April 2024, Graves removals Notice to be issued prior to planning for removal.
3	Singida	Iramba	Misigiri	1	Compensation agreement signing completed in March 2024. Graves removals Notice to be issued prior to planning for removal
4	Tabora	Igunga	Igogo	1	Compensation agreement signing completed in March 2024 Grav Graves removals Notice to be issued prior to planning for removal
5	Tanga	Muheza	Lusanga C	5	Compensation agreement signing completed in March 2024 Graves removals Notice to be issued prior to planning for removal
6	Geita	Geita	Igando	1	Valuation report approved, Compensation agreement signing expected early May 2024
<b>Total</b>				<b>15</b>	
<b>Total Unremoved Graves</b>				<b>18</b>	

# LIVELIHOOD RESTORATION

## Livelihoods Restoration Program (LRP)

### LRA 1-3: Sustainable Agriculture

Livelihoods Restoration Program has been training Project Affected Households (PAHs) in sustainable agriculture practices. One of the Sustainable Agriculture practices LRP has adopted and has been training PAHs is Conservation Agriculture. This initiative aims to equip PAHs with the knowledge and skills needed to engage in farming methods that promote long-term environmental health and economic viability.

Through training sessions and capacity-building, PAHs learn techniques such as conservation farming, soil conservation, and water management, ensuring that agricultural activities are conducted in a manner that preserves natural resources and supports sustainable livelihoods.




## Implementation progress for LRA1 -3 on Conservation Agriculture

The Livelihoods Restoration Program (LRP) successfully scoped 7,278 out of 11,18 PAHs across both the Pipeline (PPL), Project Area (PA), and Main Storage Terminal (MST) sites. During this process, key information such as PAH land parcels, crop choices for planting, and land clearing and preparation requirements were determined. This comprehensive scoping effort enables the LRP to tailor support and interventions to the specific

needs of each PAH, ensuring effective and sustainable livelihood restoration initiatives.

Out of the 7,278 PAHs scoped, 4,186 are actively engaged in LRA 1 -3 for the current planting season. Scoping activities are advancing steadily to reach all eligible PAHs, concurrently with the implementation of other program activities.

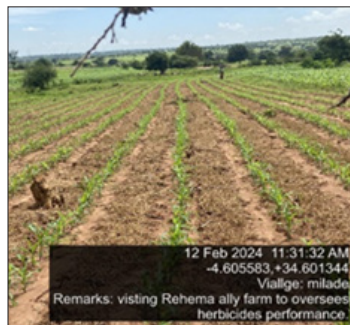

## Benefits of the Sustainable Agriculture

Advantages of Minimum Tillage	Advantages of Minimum Tillage	Advantages of intercropping
<ul style="list-style-type: none"> <li>• Reduce soil erosion.</li> <li>• Improve soil organic matter.</li> <li>• Cost saving-fuel, time, and labour cost.</li> <li>• Improves infiltration and conserves soil moisture.</li> <li>• Increase yields and income.</li> </ul>	<ul style="list-style-type: none"> <li>• Reduce soil erosion.</li> <li>• Improve soil organic matter.</li> <li>• Cost saving-fuel, time, and labour cost.</li> <li>• Improves infiltration and conserves soil moisture.</li> <li>• Increase yields and income.</li> </ul>	<ul style="list-style-type: none"> <li>• Improvement of water use.</li> <li>• Improve fertility and production.</li> <li>• Ensure food security and nutrition.</li> <li>• Increases crop yields per area.</li> </ul>



## Benefits of the Sustainable Agriculture

- Improves Soil Fertility.
- Are adoptable by small, medium, and larger farmers.
- Are adoptable by women and female headed households.
- Reduce labor inputs and time.
- Make more efficient use of on-farm and purchased resources.
- Adopters can double or thrice yields.
- Improves household food security and income.
- Improve performance of crops in dry, normal, and wetter seasons.
- Reduce soil erosion.

**Overall,** it improves livelihoods of smallholder farmers while at the same time protect the natural resource base and the environment.



# REPLACEMENT HOUSING

- A total of 297 houses for pipeline PAPs are complete and have been handed over to their respective PAPs.
- Currently, warranty works are progressing globally at 19%, with 49 houses having already undergone remedial work for identified defects, and signoffs have been collected from the PAPs, marking the completion of the one-year warranty phase for these 49 houses (refer to the table below).
- The remaining 245 houses are still within their one-year warranty period. During this time, the Project, alongside their contractors, is responsible for addressing and remedying any defects that may arise from the replacement houses.
- Warranty work involves inspecting all 297 houses for defects, remedying any identified issues, and obtaining signoffs from the PAPs after the remedial works are completed, thereby signifying the end of one-year warranty period.



## PA and Pipeline Warranty Works Progress - April 2024

PIPELINE REGIONS	WORK PACKAGES (WP)	TOTAL No. SITES	Warranty Ended	Defects not Reviewed	Defects Reviewed (Initial Inspection)	Under Repair (Remedial works)	Repairs Complete (Final Insp. & Sign Offs)	GLOBAL PROGRESS BY WP
PRIORITY AREAS	CY, MPY 5, 6, 8, 9 & 11	30	30	0	30	0	30	100%
Kagera North	WP1	40	0	40	0	0	0	0%
Kagera South	WP2 - PS3	64	46	2	62	9	49	87%
Geita	WP3	26	0	26	0	0	0	0%
Shinyanga	WP4	10	0	10	0	0	0	0%
Tabora		15	0	15	0	0	0	0%
Singida	WP5 - PS6	27	0	27	0	0	0	0%
Manyara	WP6 - PRS1	26	0	26	0	0	0	0%
Dodoma		16	0	16	0	0	0	0%
Tanga	WP7	40	0	40	0	0	0	0%
<b>TOTAL No.</b>		<b>294</b>	<b>76</b>	<b>202</b>	<b>92</b>	<b>9</b>	<b>79</b>	<b>19%</b>
<b>GLOBAL COMPLETION OF ACTIVITY</b>			<b>26%</b>	<b>69%</b>	<b>31%</b>	<b>3%</b>	<b>27%</b>	

The table delineates the advancement of warranty-related tasks across the eight distinct regions, accompanied by a parallel depiction of the overall global progress, reflecting a global progress of 19%

PROVISIONAL ACCEPTANCE CERTIFICATES - PIPELINE REPLACEMENT HOUSING CONSTRUCTION										
No of Work Packages		7			No. of PAPs		264			
Total No. of Structures		839			No. of Houses		296			
S/No	Work Package (WP)	Pipeline Region	No. of PAPs	No. of Houses	Houses Handed Over	No of PAPs Handed Over	RAP to PAP	No. PAC Issued	End of 1 Year Warranty Period	Remarks
1	WP-1	Kagera North	40	41	41	40	40	40	15-Jul-24	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
2	WP-2	Kagera South	64	67	67	64	64	64	19-Jun-24	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
3	WP-3	Geita Region	26	29	29	26	26	26	27-Jul-24	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
4	WP-4	Shinyanga Region Tabora Region	25	29	29	25	25	25	10-Aug-24	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
5	WP-5	Singida Region	27	38	38	27	27	27	15 Oct 2024	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
6	WP-6	Dodoma Region Manyara Region	42	50	50	42	42	42	13 Nov 2024	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
7	WP-7	Tanga Region	40	43	43	40	40	40	27 Nov 2024	Provisional Acceptance Certificates 100% collected warranty period has started on all houses
TOTAL NOS.			264	297	297	264	264	264		
TOTAL STRUCTURE				839	100%	100%	100%	100%		

Table references houses handed over and Provisional Acceptance Certificates Issued. (Signifies start and end of one year warranty period)

## STAKEHOLDER ENGAGEMENT – GOVERNMENT AND COMMUNITY

In April 2024, EACOP social team continued to emphasize on collective achievements, tackling challenges, and focusing on taking necessary steps to minimise or even avoid potential social risks for the project. It is paramount for EACOP to continue building relationships with key

stakeholders based on trust, while maintaining the existing ones and fostering shared values on transparency and accountability with all stakeholders involved.

### High-level Engagement and support

#### EACOP’s Participation in Parliamentarians’ Workshop

EACOP social team was honoured to be part of the EACOP delegation invited to attend a workshop organised by Ministry of Energy (MoE) for members of the Parliament of the United Republic of Tanzania. The event took place on 30th April at the parliamentary grounds in Dodoma. EACOP was challenged to present its Corporate Social

Responsibility (CSR) Strategy. The EACOP delegation, including the Managing Director, Head of Legal and Social Lead, attended the workshop. The event was also attended by representatives from TPDC and many other key people and organisations in the extractive sector.

## National NGOs (non-governmental organizations) Engagement

EACOP was invited to and actively attended the Breakfast Meeting organized by Policy Forum in collaboration with Stanbic bank on April 25th. The event centered on discussions about the recently released report by the Chief

Accountant of Government (CAG). EACOP's attendance demonstrated its commitment to engaging with non-governmental organizations (NGOs) and taking part in constructive dialogues.



Panellists and representatives from various organisations in a group photo after the debate session

## Community Safety

### THT (Tanzania House of Talent) road safety campaign

The contractor has concluded Phase 1 of Package 3 which involved conducting community awareness events in Shinyanga, Tabora, Tanga, and Manyara regions.

This month, THT is expected to complete Phase 2 of the same package which will include visiting villages in Singida, Dodoma, Kagera, and Geita region.

In making this possible, the contractor is deploying two teams, team 1 will conduct activations in Kagera and Geita while the other team will conduct activations in Singida and Dodoma region. Each team contains 13 members including a driver and a coordinator/team leader who will also be the emergency contact person, and each of them is expected to cover 53 villages.



THT Team 1 arrived in Missenyi and was received by the district focal person ready to kick off the awareness campaign



## World Safety Week

The week from 22nd to 25th April, EACOP commemorated the World Safety Week through a series of tree planting events held across various regions including Dodoma, Singida and Geita. These events symbolized EACOP's commitment to environmental sustainability and served as a poignant reminder of the importance of safety in our working environments and communities. Participating in

tree planting activities, EACOP teams contributed to the preservation of natural ecosystem and fostered a culture of safety awareness and collective responsibility through a series of presentations. This initiative not only promoted environmental conservation but also reinforced the significance of safety in all aspects of our lives, aligning with the overarching goals of World Safety Week




Photos showing EACOP's commemoration of the world safety week both in Kondoa and Singida, the event involved a symbolic tree planting exercise

## Engagement Progress


A total of 406 engagement meetings were conducted this month, reaching out to 6,057 stakeholders, of whom 2,853 (47%) were women. The cumulative total of meetings in 2024 is 1,835 meetings have been conducted from January to April by the field-based stakeholder engagement team, reaching out to 24,919 stakeholders of whom 11,039 (44%) are women.

## A graph reflecting annual engagement progress

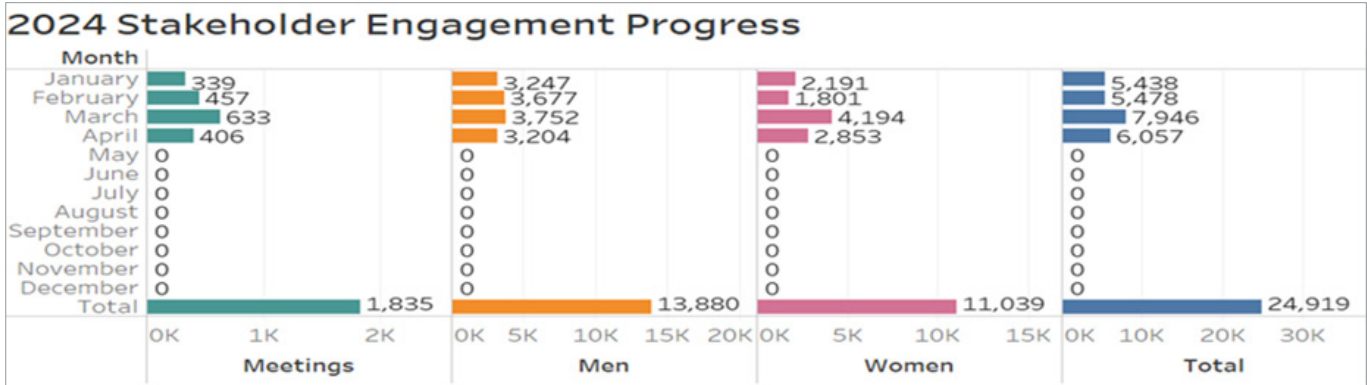

## Vulnerable Ethnic Groups Self-Identifying as Indigenous People Engagements

Engagements with vulnerable ethnic groups self-identifying as indigenous people were conducted in three regions of Manyara, Tanga and Tabora. A total of 33 meetings were held, 5 with authorities and 28 with communities. 15 meetings were conducted in Manyara, 12 in Tanga and 1 in Tabora. A total of 655 stakeholders were engaged including 378 women which is 58%.

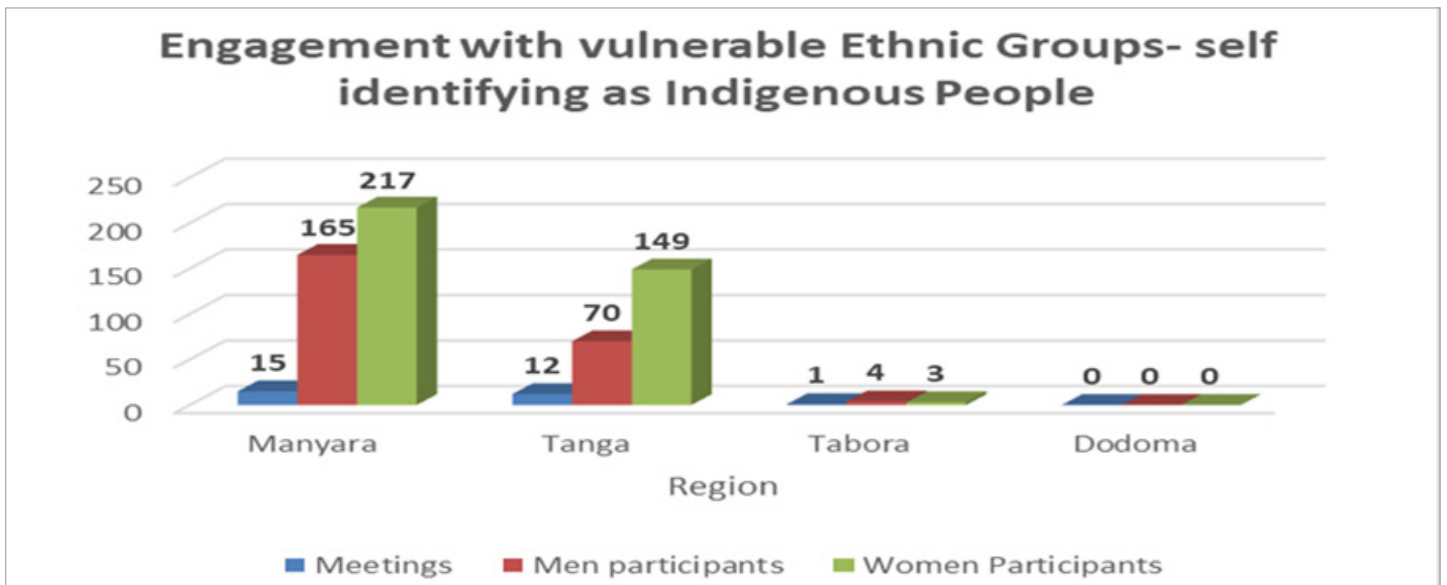

A graph reflecting engagements with Vulnerable Ethnic Groups self-identifying as indigenous people per region.


## Community Level Engagement

At the community level, 213 meetings were conducted. This includes 133 meetings with communities which brought together 4,541 participants of whom 2,359 (51%) are women. There were also 80 meetings conducted with individual PAPs reaching 337 people of whom, 69 (21%) were women.



**213**  
meetings  
conducted

### April 2024 Chart reflecting engaged community percentages per region

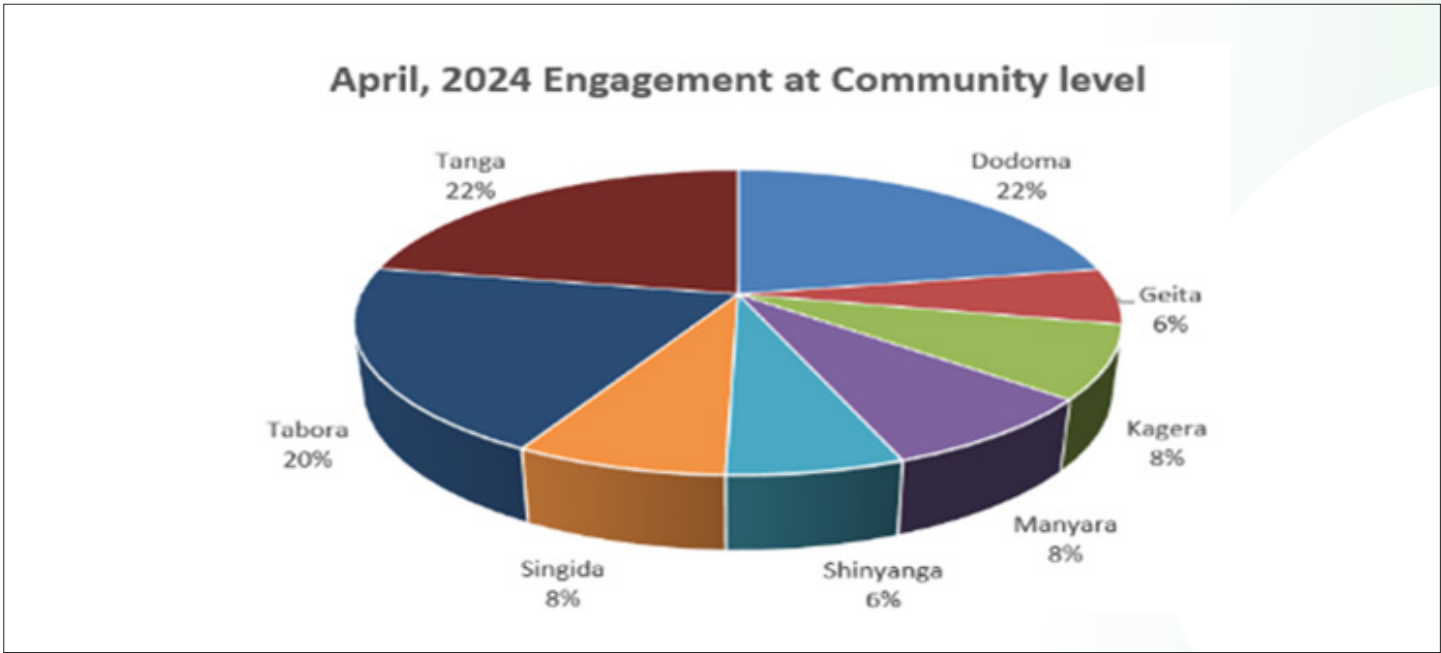


## Government & Regional Engagement

This month, EACOP managed to conduct eleven community grievance management meetings both in the field and at the Dar Es Salaam Office (HQ). This includes:

- No grievance was registered nor closed out in this month.
- Seven follow-up meetings were facilitated by the Community Relations Coordinators, Community Relations Supervisors with complainants and Land team.
- Three weekly meeting was held with the social team to discuss various issues, including grievance management.
- One post grievance closure follow-up with the complainant in Kondoa TC. This was to emphasise on the closure agreements and implementation follow up of the resolution.

## Grievance Management

### Grievance status in April 2024

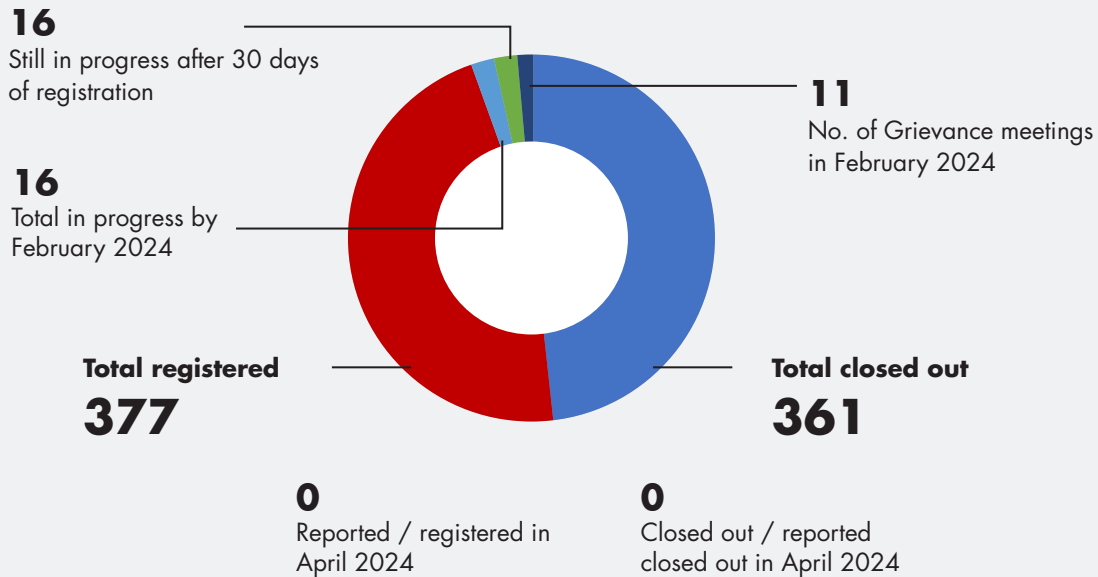

All land grievances related to land disputes rely on community-available resolution channels within the Tanzania laws for resolution. The EACOP CRCs are continually building abilities on community grievance management to local leaders. In this month of April, 25 villages have been trained, reaching 115 local leaders including 24 women.

## Gender Action Plan

This month, 213 meetings were conducted at the community level, 80 meetings with 337 PAP individuals including 69 (21%) women. 133 meetings conducted with community members in assembly and focus group discussions, out of 4,541 community members engaged, 2,359 (51%) were

women. Furthermore, the field team managed to conduct 35 women-only meetings which reaching 942 participants, this being our continued initiative to raise their levels of participation.

## PROJECT INDUCED IN-MIGRATION (PIIM)

### National Campaign

PIIM communication campaign is ongoing on radio and social media and will last until July 2024 and uses 3 communication channels: radio (national and regional), social media and newspapers

RADIO	SOCIAL MEDIA	NEWSPAPERS
<p><b>National radios:</b> Clouds FM, Radio Free Africa</p> <p><b>Local radios</b> Pangani FM (Tanga), Standard FM (Singida), CG FM (Tabora), Storm FM (Geita), Kwizera FM (Kagera), Dodoma FM (Dodoma), Gold FM (Shinyanga), ORS FM (Manyara)</p>	<p>YouTube LinkedIn Facebook Twitter Instagram</p>	<p><b>Swahili Newspaper:</b> Mwananchi <b>English Newspaper:</b> the Guardian EACOP website.</p>

The campaign is to encourage individuals to consider their personal situation and gather accurate information before deciding to relocate or leave their current income generating activities. This campaign is focused on:

- Job opportunities in the different job categories (unskilled, semi-skilled and skilled).
- Labour requirements and thereby discourage spontaneous influx towards project work sites and

- The risk of fraudulent advertisements regarding EACOP recruitment procedures.

A media monitoring exercise is conducted throughout the campaign implementation periods: Jul-Oct 23, Nov-Jan 24, Feb-April 24, May-July24. So far, radio adverts were well appreciated by the listeners giving a high interest in the subject and the need to get further information.



## IMAGERY ACQUISITION

The project acquired imagery on a quarterly basis to monitor change and in addition, an analysis report is also provided by the contractor, Kayrros, since September 23. This report covers all the changes detected around each MCPY (Main Camp and Pipe Yard) and the new buildings are categorised in 2 main groups: Public building (schools, church,...) and others. All these changes are documented by the PIIM coordinators' field visits with the support of the field team. These changes are also correlated with the data provided by the authorities within the quarterly PWG (PIIM Working Group) meetings in the hotspot locations (Tanga, Nzega, Kahama and Bukombe).

Some new food/beverage shops and transportation businesses appear in some areas (ex:Sojo, Ushirombo) to meet the EACOP workers needs and not for some new comers from other Tanzanian regions. So far thanks to the national campaign and the stakeholder engagement meetings, no major long-term PIIM impact has been observed.

Thanks to clear information given to the communities by the EACOP field team in collaboration with our contractors and also thanks to the collaboration with local Authorities, in-migrants seeking unskilled jobs decided not to stay, understanding that 100% of unskilled jobs were for project-affected communities members in priority.



# REGULATORY COMPLIANCE


## Permitting in Tanzania

The type of approval application for Importation of Electronic Communication Equipment's with TCRA is ongoing, and we are sorting out the required documents for the application.


Monitoring of active sites to ensure compliance with permit requirements and regulations, promoting efficient execution of projects.

Follow-up with all contractors to comply with CRB (Contractor Registration Board) and ERB (Engineers Registration Board) requirements is ongoing.

## GV-All Permits Acquired by L1 Contractors

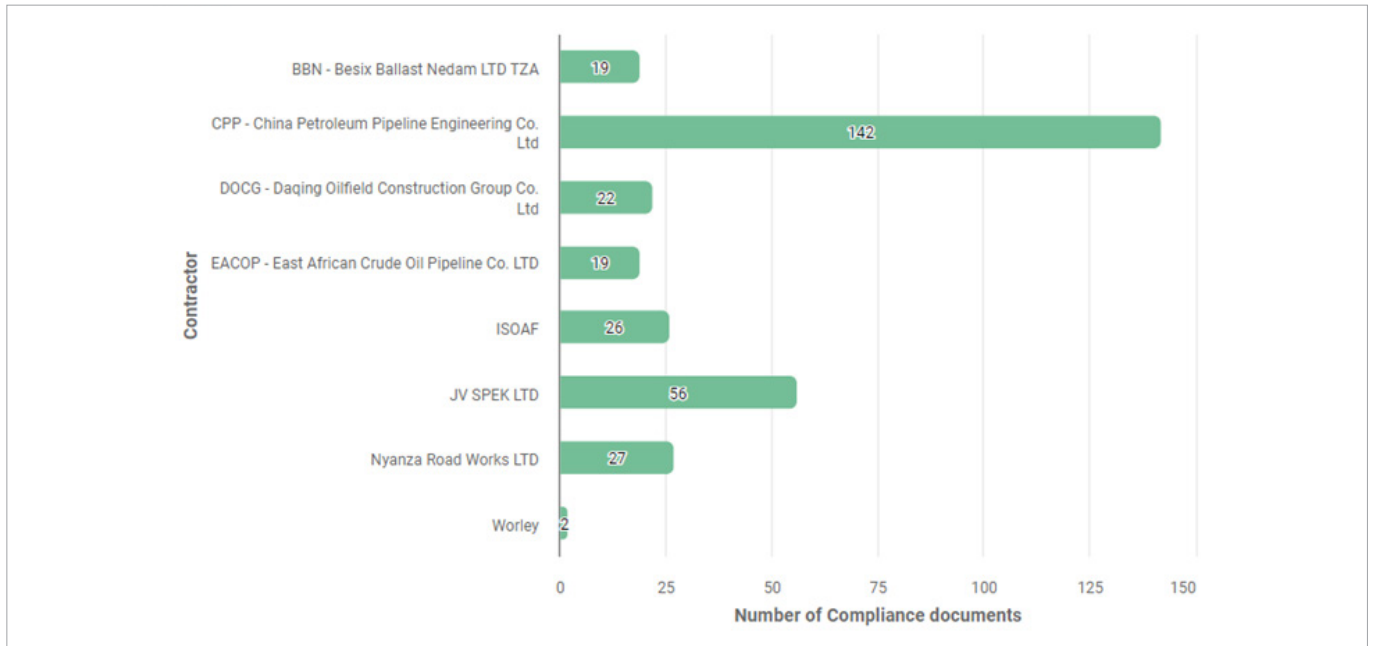

## GV-Permits Conditions Tracking Progress ...

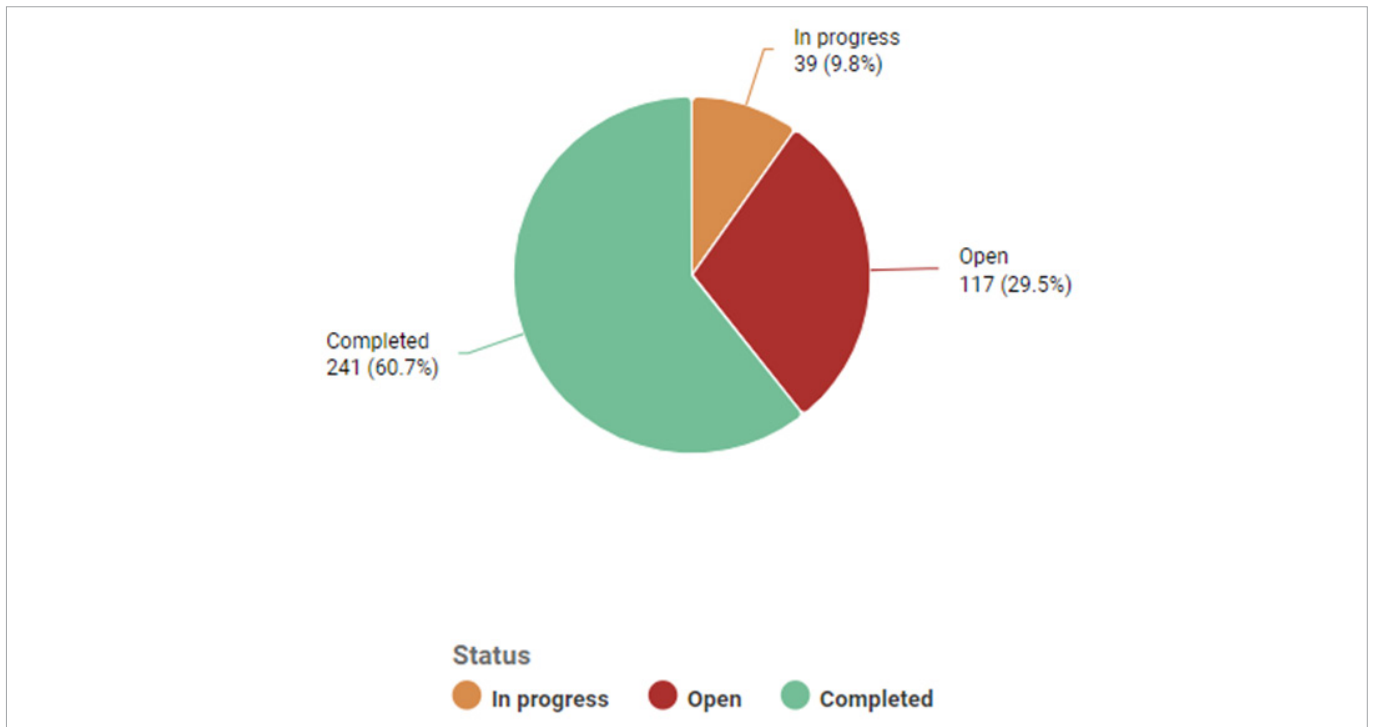

Building permit applications for permanent facilities such as offices, warehouses, power generators, etc. at MST in Tanga City Council and the Pressure Reduction Station at PRS2 in Handeni were submitted on April 22nd and 23rd, 2024, respectively.







Submission of Building Permit Application for MST at Tanga City Council

## Regulatory Compliance and Assurance

To ensure complete assurance monitoring, keep close monitoring of all non-compliances and take immediate action to address any pending actions.

### GV-Compliance by Project Area

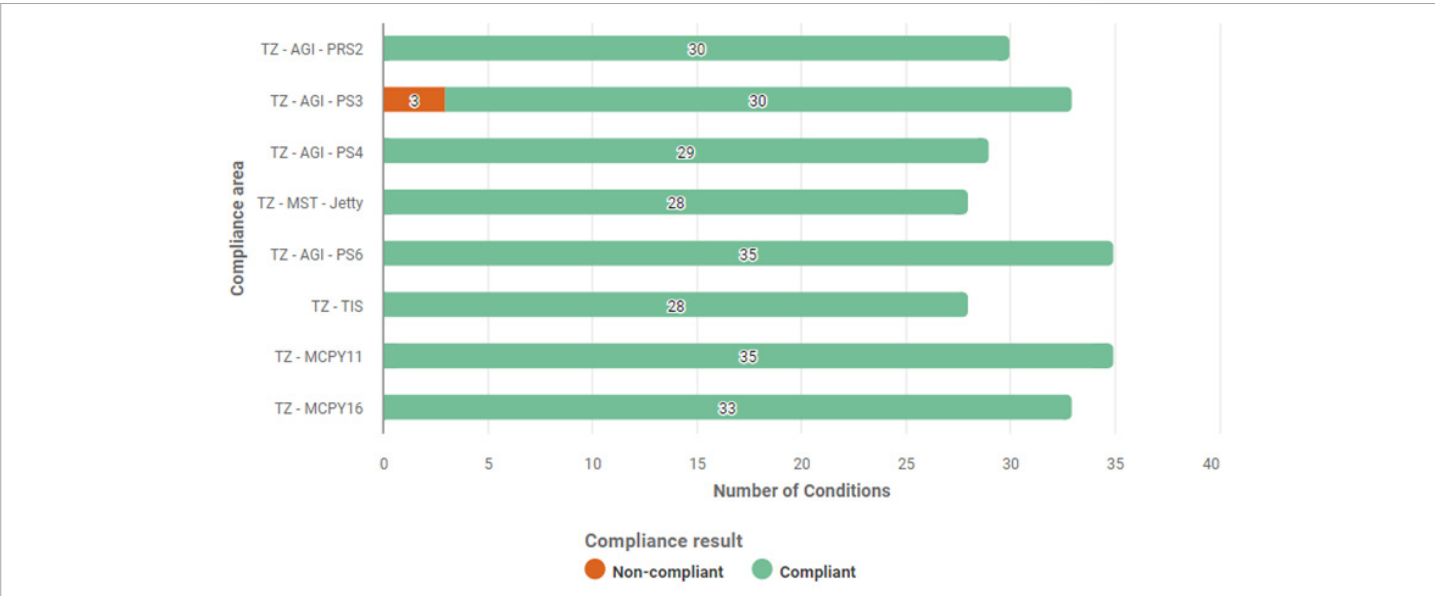



EAST AFRICAN  
**CRUDE OIL  
PIPELINE**



First Crosshead Installation

POW #041 – 13/04/2024



Ongoing Launching Girder Assembly

POW #042 – 20/04/2024

TANZANIA - Tanga Jetty

### **EACOP Internal Communications**

Human Resources and Corporate Affairs Department  
East African Crude Oil Pipeline (EACOP) Ltd.  
Msasani Peninsula plot no 1403, block 1, house 7.  
Brains Avenue, off chole road.  
P.O.Box. 23139, Dar es Salam, Tanzania.  
Email: [infor.tz@eacop.com](mailto:infor.tz@eacop.com)

©2023 All Rights Reserved.  
No part of this publication should be reproduced, altered in a whole or part without prior written notice from the East African Crude Oil Pipeline Management.

