

# EACOP TANZANIA

## Monthly Updates

**SUCCESSFUL DELIVERY OF  
THE FIRST 100KM LINE  
PIPES IN TANZANIA**





# CONTENTS

<b>03</b>	<b>INTRODUCTION</b>	
<b>04</b>	<b>CONSTRUCTION</b>	
<b>06</b>	<b>LAND &amp; SOCIAL</b>	
	<b>LAND ACQUISITION UPDATES</b>	<b>6</b>
	Compensation Agreements Signing	6
	Transitional Support Services	7
	Pipeline Relocation Assessment and Support	8
	Handover of Replacement Houses	9
	Pipeline Grave Removal	9
	Pipeline Cadastral Survey	10
	<b>LIVELIHOOD RESTORATION</b>	<b>10</b>
	Livelihoods Restoration Program (LRP)	10
	VUNA Agribusiness: LRA 1-3 (Land preparation and planting, Maize Improvement and Crops diversification)	10
	Conservation Farming Unit (CFU) Contractor Kickoff of LRA 1-3 (Land preparation and planting, maize improvement, and crops diversification)	11
	<b>REPLACEMENT HOUSING</b>	<b>11</b>
	<b>STAKEHOLDER ENGAGEMENT – GOVERNMENT AND COMMUNITY</b>	<b>13</b>
	High-level CSO Engagement	13
	Engagements with Vulnerable Ethnic Groups Self-Identifying as Indigenous People	14
	Grievance Management	15
	EACOP Toll free number	15
	<b>HUMAN RIGHTS</b>	<b>15</b>
	Communication	15
	<b>PROJECT INDUCED IN MIGRATION</b>	<b>16</b>
	Social Media Messages	18
<b>20</b>	<b>REGULATORY COMPLIANCE</b>	
	Permitting in Tanzania	20
	Regulatory Compliance and Assurance	21



## INTRODUCTION

This update aims to provide the eight Regional Authorities and 27 District/Town/City Councils hosting the East African Crude Oil Pipeline (EACOP) Project in Tanzania (refer to figure 1 below) with a status report on ongoing activities as of October 2023.

The goal is to convey practical information about the current field activities, facilitating engagement and keeping the Regional Authorities informed.




## Replacement Housing Handover Ceremony





# PROJECT CONSTRUCTION

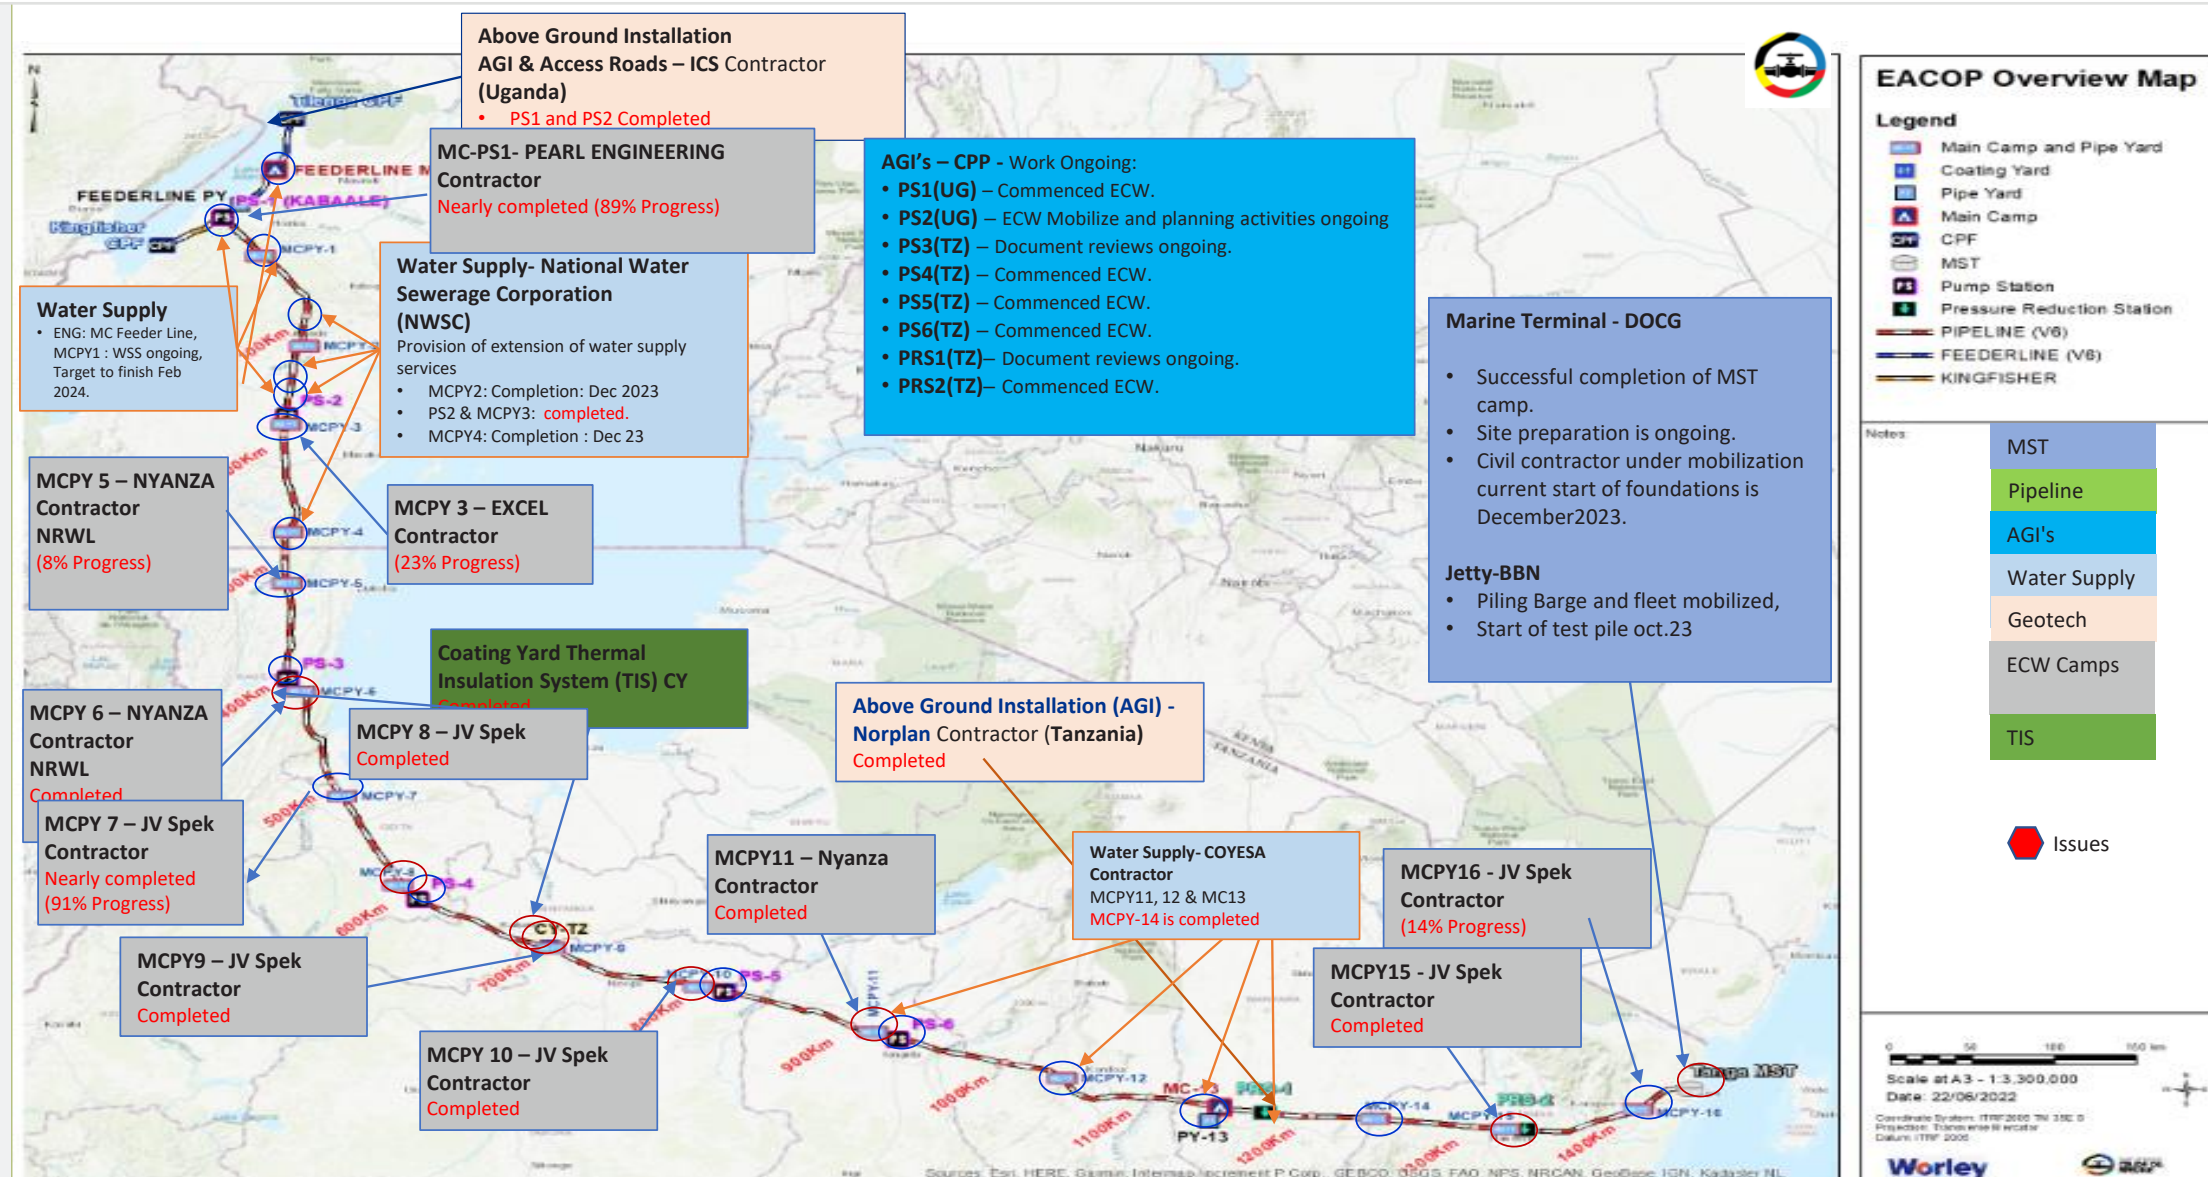

## Pipeline, Early Civil Works (ECW) of the Main Camps and Pipeyards (MCPY)

- CPP Pipeline Crossings Survey (57 sites) continues, completion in November 2023.
- Project Lot 2 Main Line Block Valve (MLBV) access road survey completed October.
- JV Spek Early Civil Works (ECW) MCPY-16 continues, completion February 2023, works progress affected by Elnino rains.
- CPP MCPY-15 camp construction is ongoing.
- ECW MCPY-10, 09, 08, 06& 11 is completed, all sites handed over to CPP.
- JV Spek ECW MCPY-07 completed, site to be handed over to CPP early December 2023
- Nyanza Roads ECW MCPY-05 continues, completion in May 2024, works progress affected by Elnino rains.
- Cultural Heritage inductions by COMPANY Cultural Heritage Lead at MCPY-15 as part of pre-work start inductions.

- CPP courtesy calls with Regional, District, and Ward authorities, and start of routine community engagements at village and hamlets at MCPY-15 activities. All engagements led by CPP with COMPANY support.

## Above Ground Installation (AGI): Pump Stations (PS) & Pressure Reduction Stations (PRS)

- CPP start PS 5 (Igunga) early civil works site clearance activities
- CPP start PRS 2 (Handeni) early civil works site clearance activities
- CPP mobilise to PS4 (Bukombe) for early civil works site clearance activities
- CPP mobilise to PS6 (Sngida) for early civil works site clearance activities
- Cultural Heritage inductions by COMPANY Cultural Heritage Lead at these AGI as part of pre-work start inductions.
- CPP courtesy calls with Regional, District, and Ward authorities, and start of routine community engagements at village and hamlets at AGI activities. All engagements led by CPP with COMPANY support.
- CPP local workforce recruitment started at PS5, PRS-2, MCPY-15 and will start at PS4 and PS6 in November.

## Thermal Insulation System (TIS) - the Coating Yard facility.

- WASCO ISOAF continues preparation of the pipe coating facility at the TIS to receive the future pipe for coating, night shift work will start to support this activity.
- WASCO ISOAF continues construction of the TIS camp facilities, utilities and services to accommodate the TIS workforce and manage the coating yard operations.
- WASCO ISOAF community awareness raising on road safety and snake awareness (by TASCEA), providing training to communities on the community based social and environmental monitoring.
- WASCO ISOAF continue routine engagements with all communities within their area of direct influence, with COMPANY support.

## Main Storage Tanks & Terminals (MST)


- DOCG continues site preparation for the main construction phase.
- DOCG and COMPANY MST Site representatives now based at the DOCG MST construction camp.

- DOCG continues routine engagements with all communities at the Chongoleani peninsula communities with COMPANY support, in collaboration with BBN (Jetty construction Contractor) to promote information sharing and collaboration on EACOP construction activities at MST and Jetty for impacted communities.
- Visit by Traditional Leaders to the MST site 23 October.

## Jetty

- BBN started marine test piling activities at the agreed locations. BBN are based at Tanga Port facility.
- BBN completed local recruitment of workers that successfully completed marine training for working on BBN vessels during jetty construction.
- BBN engaging Chongoleani peninsula communities on the marine operations activities, awareness of BBN marine environmental management during test piling and marine operations is especially important for the fishermen of Putini and Chongoleani.



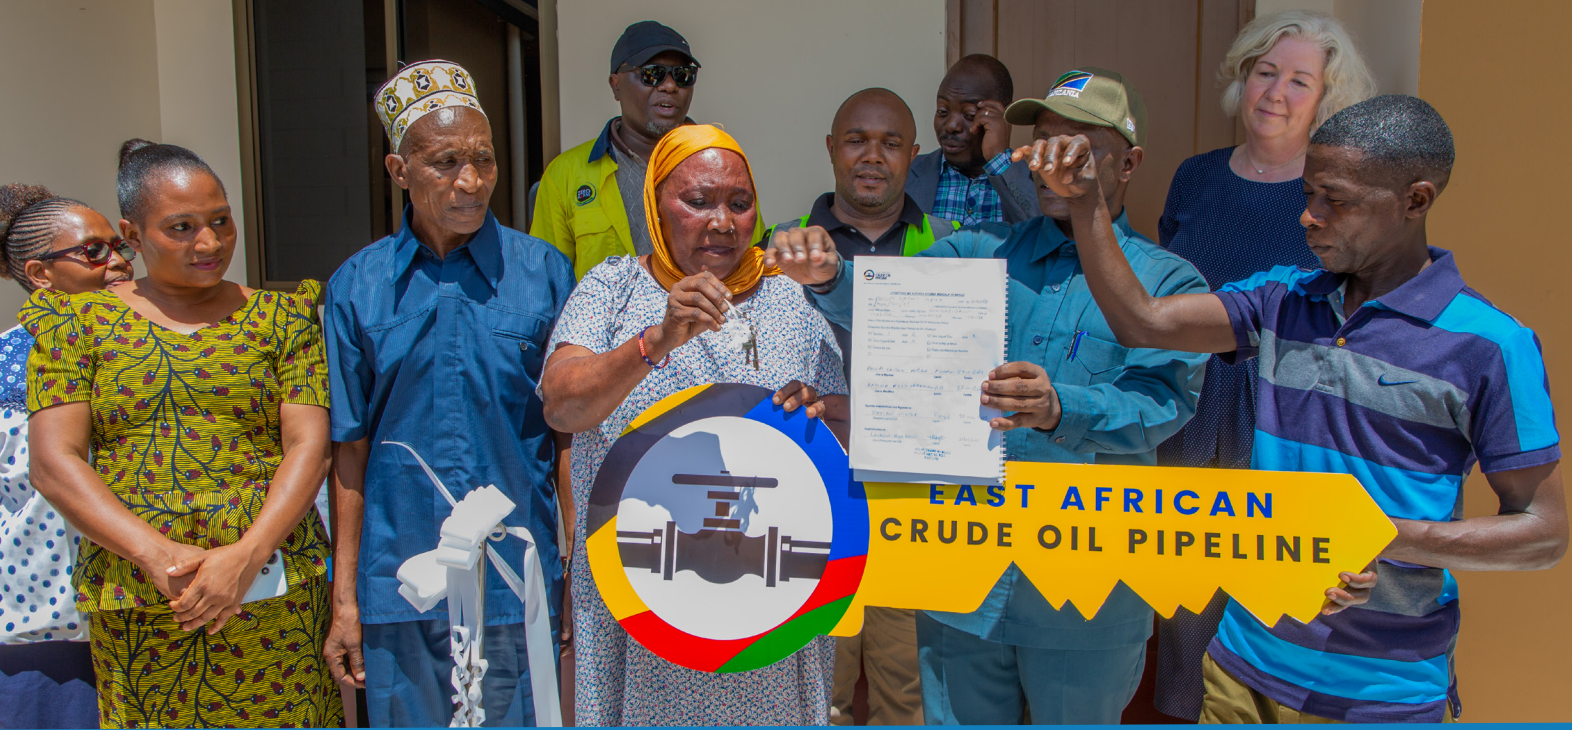

# LAND & SOCIAL

## LAND ACQUISITION UPDATES

### Compensation Agreements Signing

As of November 2023, 9,433 out of 9,514 (99%) pipeline Project-Affected Persons (PAPs) have completed compensation agreement signing, and all have received their compensation.

An Escrow review panel has been assembled to discuss the due diligence of an absent PD PAP from Geita who claimed her entitlements one year after

the EBCA process. The escrow panel provided the green light for the EBCA to proceed. An Entitlement Briefing was conducted on 2nd December 2023, and Compensation Agreement signing is expected on 18th December 2023.

### Progress Metrics: Compensation Agreements signing (Pipeline and Above Ground Installations)

Region	Number of PAPs Economically Displaced and Physically Displaced	Number of Compensation Agreement Signed (Pipeline & Above Ground Installations)	Unsigned Compensation Agreements. (Pipeline & Above Ground Installations)	Number of Paid PAPs (Pipeline & Above Ground Installations)
<b>Kagera</b>	2,316	2,306	10	2,306
<b>Geita</b>	1,468	1,455	13	1,455
<b>Shinyanga</b>	619	609	10	609
<b>Tabora</b>	945	938	7	938
<b>Singida</b>	1,296	1,287	9	1,287
<b>Dodoma</b>	816	810	6	810
<b>Manyara</b>	474	468	6	468
<b>Tanga</b>	1,580	1,560	20	1,560
<b>Total</b>	<b>9,514</b>	<b>9,433</b>	<b>81</b>	<b>9,433</b>

### Transitional Support Services

First round actual food baskets distribution completed delivered to seven regions of Kagera, Geita, Shinyanga, Tabora, Singida, Dodoma and Manyara. Actual food baskets deliveries for Tanga region to commence in December 2023.


November Cash allowance transfers completed for zone 1 and 3 regions (Kagera, Geita, Shinyanga and Tanga regions). Cash allowance transfers for the remained regions to proceed in December 2023.



Project Affected Person (PAP) after receiving his November food basket in Kondoa District




## Pipeline TSS Food Distribution - 1<sup>st</sup> Round

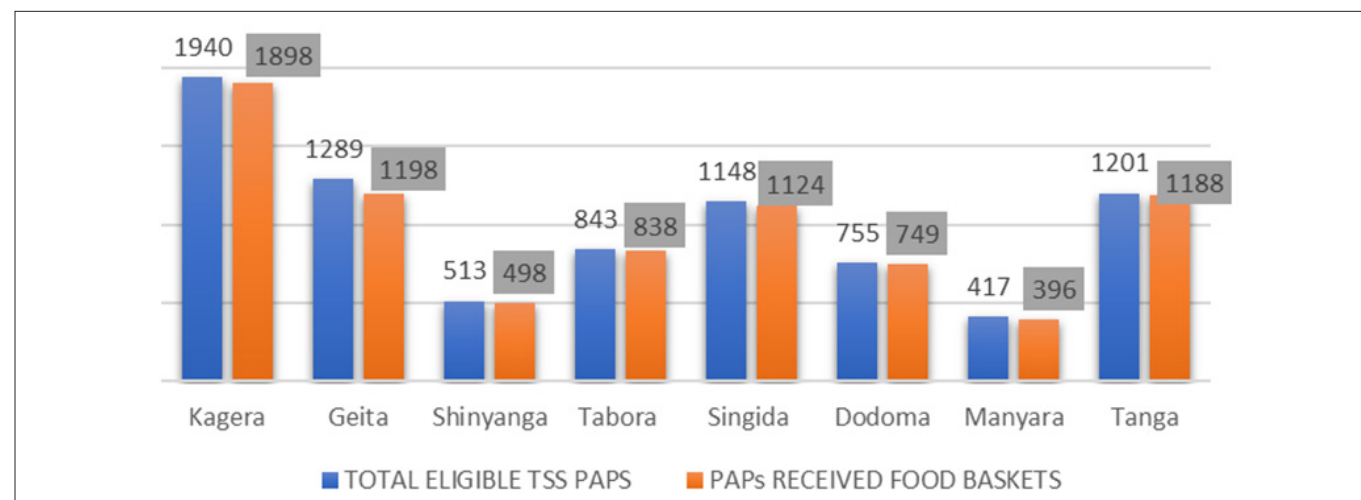

## Pipeline Relocation Assessment and Support

As of the latest update, 9,513 out of 9,514 Pipeline Project-Affected Persons (PAPs) have completed relocating from the project area. However, three PAPs have not yet finished relocating.

Specifically, one PAP at Sagida Village, Nzega District, Tabora Region, is awaiting additional relocation support to complete the relocation of the spiritual site. Additionally, two PAPs at Ilindi Village, Kahama District, Shinyanga Region, are in the process of relocating surface mining facilities.



**9,513**  
completed relocations

### Relocation support updates

RELOCATION PROGRESS				
S/NO.	Regions	PAPS	Completed relocation	% Progress
1	Kagera	2,316	2,316	100%
2	Geita	1,468	1,468	100%
3	Shinyanga	619	616	99.5%
4	Tabora	945	944	100%
5	Singida	1,296	1,297	100%
6	Dodoma	816	816	100%
7	Manyara	474	474	100%
8	Tanga	1,580	1,580	100%
<b>Total</b>		<b>9,514</b>	<b>9,511</b>	<b>99.9%</b>

## Handover of Replacement Houses

263 out of 263 Pipeline physically displaced PAPs who selected replacement houses (RH) have received and completed relocating to their new replacement houses.

The handover ceremony of the last replacement house was successfully conducted at Songakibaoni village, muheza District, Tanga region on 28th November 2023.



Hon. Colonel Maulid Sulumbu-Mkinga's District Commissioner; handing over house keys to PAP Philipo Gaitai Mpika and his wife on 28th November 2023.

### Pipeline Replacement Housing, Handover progress:

S/NO.	Regions	No of Physically Displaced PAPs	PAPs relocated to Replacement Houses.	% Progress
1	Kagera	106	108	100%
2	Geita	23	28	100%
3	Shinyanga	10	12	100%
4	Tabora	15	17	100%
5	Singida	27	38	100%
6	Dodoma	17	20	100%
7	Manyara	24	30	100%
8	Tanga	41	43	100%
<b>Total</b>		<b>263</b>	<b>296</b>	<b>100%</b>

## Pipeline Grave Removal

1,083 out of 1,087 (99.6%) Pipeline Graves have been removed. 4 graves confirmed as not removed due to: 1 grave avoided so to be removed from figures, 1 incomplete ritual performance in Geita, 1 family conflict in Singida over the impacted assets including grave, 1 unpaid compensation for grave in Muleba.

Arrangement for removal of the remaining 3 graves ongoing.

Supplementary valuation field work for seven newly claimed graves completed in Tabora and Singida regions.



**1,083**  
Pipeline graves have been relocated to sites selected by grave owners.



## Pipeline Cadastral Survey

The Ministry of Land, Housing, and Human Settlement Development (MLHSD) and the Tanzania Petroleum Development Corporation (TPDC), with the support of EACOP personnel, have conducted a cadastral survey exercise across all eight project-affected regions. The fieldwork exercise has been completed 100%.

The preparation of the Right of Occupancy in progress.



## LIVELIHOOD RESTORATION

### Livelihoods Restoration Program (LRP)

#### PPL implementation.

### VUNA Agribusiness: LRA 1-3 (Land preparation and planting, Maize Improvement and Crops diversification).

As of November 2023, the implementation of LRA 1-3 is underway in Kagera, Tabora, and Shinyanga for G1-4. Meetings have been conducted to disseminate crucial information about entitlements to eligible households affected by the project. Further details on the number of Project Affected Households (PAHs) prepared for planting this season will be communicated later. Progress is evident in Module 1 & 2 training, land preparation, planting, maize improvements, and crop diversification.

In Kagera, Module 3 training (crop protection) for LRA 1-3 has been successfully completed. The crops planted, including maize, bananas, and beans, are exhibiting robust growth. To bolster crop disease management, Module 3 training on crop protection has been conducted. A noteworthy 841 out of 1847 PAHs (45.5%) have undergone training in Module 3 on crop protection. Continuous extension services from field-based staff are being provided to support PAHs in their agricultural endeavors.



Photo 1: Contractor Extension Officer conducting crop health monitoring at Bulifani Village in Missenyi District -Kagera.



Photo 2: EACOP coordinator monitoring maize growth and impacts of waterlogged area to crops – Bulifani village in Missenyi District Kagera region.



Photo 3: PAPHs Deogratius Rwehumbiza, enjoying his first banana bunch from the EACOP supported banana planted in first season of intervention. - Bulifani village in Missenyi District Kagera region.

## Conservation Farming Unit (CFU) Contractor Kickoff of LRA 1-3 (Land preparation and planting, maize improvement, and crops diversification)

The inaugural meeting for the LRA 1-3 contract, focusing on work packages 3 and 4, was convened in Dar to signal the initiation of these activities for eligible Project Affected Households (PAHs) in Singida, Manyara, Dodoma, and Tanga.

CFU has been awarded the contract for work packages 3 and 4 to execute the LRA 1-3 implementation across the specified regions. The LRA scoping is slated for early December to pave the way for the commencement of agricultural activities. Due to

the impact of El Niño, the Tanga region witnessed an earlier onset of rainfall than originally projected. Consequently, the contractor has opted to defer the commencement of agricultural activities for this season until February 2023.

The postponement aims to allow sufficient time for scoping and planning, ensuring a well-prepared engagement with Project Affected Households (PAHs) for the first season in Tanga.

### LRA4 (Poultry improvement program)

Zakayo Daudi, a Project Affected Person a resident of Njoro village in the Kiteto district, chose to engage in poultry farming. Initially, he received five chicks from EACOP and underwent training in enhanced poultry farming practices.

Demonstrating dedication to his venture, Zakayo expanded his chicken coop to accommodate a larger flock. Presently, he owns a total of 50 chickens, acquired through the proceeds from selling maize with support from EACOP. His overarching goal is to supply eggs and chicken meat to the camp located in Kiteto as part of his long-term plan.



Photo 4: Zakayo Daudi's poultry project showcases his progress, initially received 5 chickens from EACOP and subsequently expanding his flock to 50. His ultimate objective is to supply eggs and chicken meat to the EACOP camp.

## REPLACEMENT HOUSING

- All 296 houses are complete and have been handed over to their respective PAPHs with a global construction progress at 100%.
- Replacement houses have been fully constructed in regions of Kagera, Geita, Shinyanga, Tabora, Singida, Dodoma, Manyara and Tanga.
- A total of 1147 continuous kilometres of pipeline have been cleared of all housing activities.
- An additional 57 kilometres, which are not in continuous succession, have been cleared of all housing-related activities.



**296**  
houses have  
been handed over

### Notable progress in the month of November 2023 includes:

- The handover of 34 houses to their respective PAPHs.
- Completion of house construction in the region of Tanga.

- The conclusion of the house construction marks the beginning of a one-year warranty period. During this duration, the Project, along with their contractors, shall be responsible to remedy any defects that may arise from the replacement houses.




## Pipeline Replacement Housing Construction

No of Work Packages		7		No. of PAPS		263	
Total No. of Structures		838		No. of Houses		296	
S/No	Work Package (WP)	Pipeline Region	No. of PAPS	No. of Houses	Houses Handed Over	No of PAPS Handed Over	
1	WP-1	Kagera North	40	41	41	40	
2	WP-2	Kagera South	64	67	67	64	
3	WP-3	Geita Region	25	28	28	25	
4	WP-4	Shinyanga Region, Tabora Region	25	29	29	25	
5	WP-5	Singida Region	27	38	38	27	
6	WP-6	Dodoma Region, Manyara Region	42	50	50	42	
7	WP-7	Tanga Region	40	43	43	40	
<b>TOTAL</b>			<b>263</b>	<b>296</b>	<b>296</b>	<b>263</b>	
<b>TOTAL STRUCTURES</b>				<b>838</b>	100%	100%	



Replacement Housing Ceremony

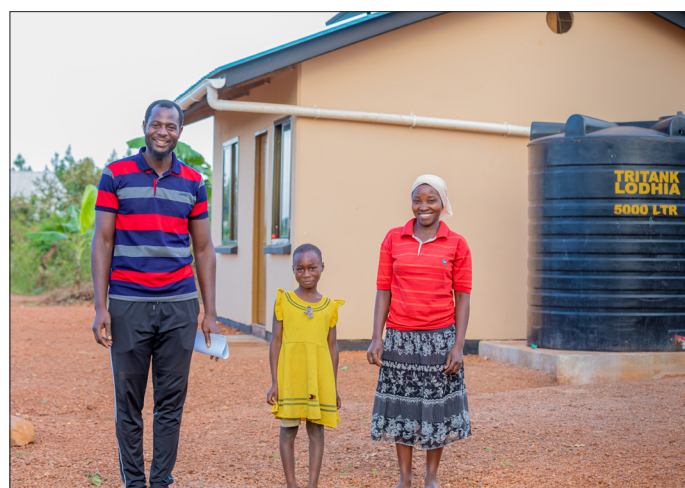

## STAKEHOLDER ENGAGEMENT – GOVERNMENT AND COMMUNITY

The main engagement topic for this month is still transitional support services for pipeline PAPS. A total of 334 meetings were held in various communities, bringing together 7,125 stakeholders out of whom 36% were women.

The focus of engagement was on general project status updates, supporting different field activities including courtesy meetings to introduce CPP teams at regional, district, ward and village levels, in areas where camp construction is due to start soon example

MCPY 15 Handeni Tanga. Engagements supporting RAP activities such as the ongoing pipeline cadastral Survey, Transitional Support Services (TSS), and Biometric registration.

In October, EACOP's social team continued its efforts to engage with various groups of stakeholders in the project-affected communities (PAC). Some of these stakeholders include religious leaders, NGOs as well as small business owners.

Source: Stakeholders data collection Tool

Area/ Level	Meetings	Number of Persons	Women Pax
<b>A Regional</b>	18	65	14
<b>B District</b>	67	289	68
<b>C Ward Authority</b>	18	98	27
<b>D Village Authority (VDC, VEO, VC, Village Committees)</b>	78	254	43
<b>E Meeting with Authorities</b>	181	706	152
<b>F PAC (Village Assembly, Small Group, FGD)</b>	89	4,963	1,948
<b>G PAP&amp; Individual Meeting</b>	63	1,345	435
<b>H Meetings with communities</b>	152	6,308	2,383
<b>Total</b>	<b>333</b>	<b>7,014</b>	<b>1,953</b>

### High-level CSO Engagement

EACOP was honored to participate in the largest gathering of civil societies in Tanzania. The CSO week sets the stage for different actors from both the public and private sectors, for high-level conventions on development in Tanzania. This year's event focused on the role of technology and the impact it has on society, both now and in the near future.

An estimated 1000 people from the public and private sectors participated in the various interactive sessions, both physically and through online platforms. More than 120 national civil societies and non-state organizations.



## Engagements with Vulnerable Ethnic Groups Self-Identifying as Indigenous People

Twenty-five meetings were held with Vulnerable Ethnic Groups self-identifying as Indigenous People where four hundred thirty-four stakeholders were reached of whom 134 (29%) were women. Among those meetings, one was a quarter-three traditional leaders meeting which was held at Arusha between 26th and 28th October. This was preceded with a project trip to Tanga and a visit at MST, the Jetty area and the replacement house by fifteen traditional leaders, NGO representatives (UCRT,

Pingos Forum and Paicodeo), Advisor and District Focal person from Handeni, Kilindi, Simanjiro, Kiteto, Kondo, Hanang, and Igunja.

Apart from general project update, the traditional leaders were capacitated on TSS, Zero Harm safety Cultures, project Induced Immigration as well as Human Rights. Three NGOs (UCRT, Paicodeo & Pingos Forum) supporting capacity building of this group together with advisors attended the meeting.

Below is the summary of October Vulnerable Ethnic Groups Engagement at different level

Area/ Level	Meetings	Number of Persons	Women Pax
<b>A Regional</b>			
<b>B District</b>	1	111	29
<b>C Ward Authority</b>	1	2	0
<b>D Village Authority (VDC, VEO, VC, Village Committees) (A+B+C+D)</b>	2	3	2
<b>E Meeting with Authority</b>	4	9	1
<b>F PAC (Village Assembly, Small Group, FGD)</b>	8	125	32
<b>G PAP&amp; Individual Meeting</b>	17	339	102
<b>H Community (F+G)</b>	0	0	0
<b>I Total (E+H)</b>	17	339	102

Source: Stakeholders Data Collection Tool




Traditional Leaders Visit at EACOP Foundation Stone



BBN staffs pose in a photo with Taturu & Akie Ladies at a Tanga Port during the Visit

## Grievance Management

In October No grievance was recorded, however, we did manage to close two grievances one related to the RAP implementation process and the other one on payment of service levy. Communities are always reminded of EACOP's grievance procedure during broader engagement sessions facilitated by social teams as well as during other ongoing field activities.

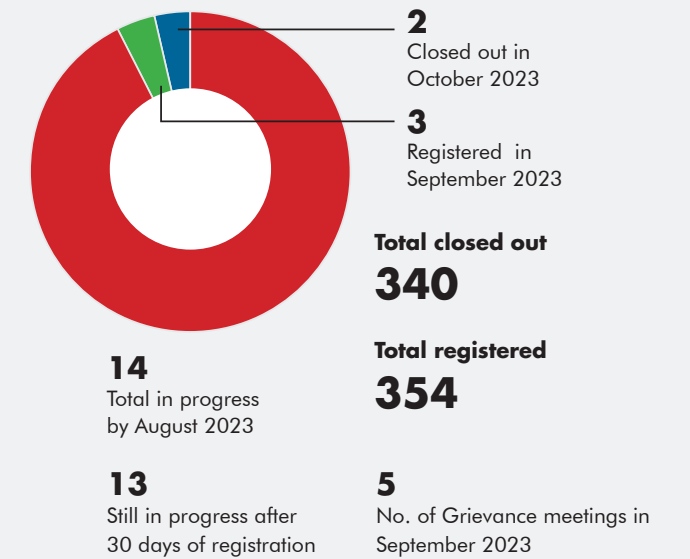


## EACOP Toll free number



17

Calls received

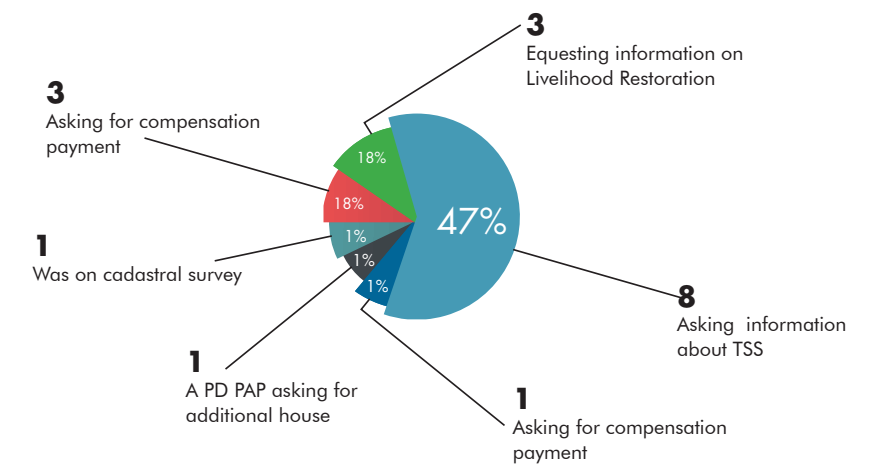

## HUMAN RIGHTS

In November, a Gender Equality & Social Inclusion policy and a Gender Action Plan (GAP) have been

developed. The GAP implementation and the monitoring & Evaluation will be followed up as from January 2024.

### Communication

EACOP participated to the commemoration of the International Human Rights Day 2023 and the 75th years Universal Declaration of Human Rights of 1948, event organized by the East African Human Rights Institute at the University of Dar Es Salaam. The EACOP management was also invited by the Tanzania Episcopal Conference to their event commemorating 75 years of

UDHR and the role of religious leaders in promoting and respect of human rights in the country. It was an opportunity to share EACOP human rights actions align with the UN Guiding Principles in the Project framework: staff trainings on Human Rights, actions implemented to address the Human Rights Due Diligence report recommendations (Dec 2022).



## PROJECT INDUCED IN MIGRATION

The PIIM Working Group (PWG) meetings were held in November in the 3 identified hotspots in the report issued in 2019 (PIIM Situation Analysis Report: CY/Nzega, Bukombe, and Chongoleani Peninsula) and also in Kahama because of the potential impacts due to

the Kakomgwa road use for the pipeline transportation. Indeed, all pipelines are transported from the Dar Es Salaam port to Sojo Coating Yard plant to be equipped with the Thermal Insulation System (TIS) and therefore the truck traffic will increase considerably.

**In the below table sheets, the list of all attendees is given for each location with the number of attendees and the meeting date.**

### TANGA 27TH NOV 2023

1	WEO Chongoleani ward
2	Police Officer Tanga City
3	Economist - Tanga City Council
4	Human Resources Department (HRD) - Tanga City
5	Senior Community Development Officer & District Focal Person DFP
6	Marine Storage Terminal Site REP
7	DOCG Social Manager
8	EACOP Community Relationship Coordinator (CRC)
9 &10	2 EACOP Community Relationship Supervisor (CRS)
11	Human Rights and Project Induced In Migration Manager – TZ & UG
12	EACOP PIIM Coordinator

### NZEGA 29TH NOV 2023

1	EACOP CRC Tabora
2	District Administrative Secretary - DAS Nzega
3	Office Commander District - OCD Nzega
4	District Immigration Officer - DIO Nzega
5	Village executive officer - VEO Sojo
6	DPLO Nzega
7	Ag. Ward Executive Officer - WEO Igusule
8	Village Chairperson - VC Sojo
9	EACOP HURI and PIIM Manager – TZ & UG
10	EACOP PIIM Coordinator TZ

### KAHAMA 28TH NOV 2023

1	Isaka Village executive officer (VEO)
2	Isaka Village chairperson (VC)
3	Kagongwa ward executive officer (WEO)
4	Kagongwa Mtaa chairperson
5	Kagongwa Mtaa executive officer (MEO)
6	Msalala ward executive officer (WEO)
7	Gembe Village chairperson (VC)
8	Gembe Village executive officer (VEO)
9	Ipona Mataa executive officer (MEO)
10	Ipona Mataa executive officer (MEO)
11	Kishima Mtaa chairperson (VC)
12	Kishima Mataa executive officer (MEO)
13	Officer Commander District (OCD)
14	District Health Officer (DHO)
15	District Environment Officer (DEO)
16	District Focal Person (DFP)
17	EACOP CRC Shinyanga
18	EACOP HURI and PIIM Manager – TZ & UG
19	EACOP PIIM Coordinator

### BUKOME 01ST DEC 2023

1	Bukombe District Administrative Secretary
2	Bukombe District Immigration Officer
3	Bukombe District Health Officer
4	Bukombe District Council Environmental Officer
5	Bukombe District Council Community Development Officer
6	Bukombe District Security Officer - DSO
7	Bukombe Ward Executive Officer
8	Bukombe Village Executive Officer
9	Bukombe Village Chairman
10	Bukombe Officer Commander District OCD
11	Bukombe District Labour officer - DHRO
12	Bukombe - DPCO
13	Bukombe - DFP
14	EACOP PIIM Coordinator TZ



These meetings allowed to share information on the Project activities progress and also on PIIM criteria evolution such as in-migrants arrival in the area, opening of new businesses (guesthouses, restaurants, bars, food shop...), safety road management, security incidents, trend of patient number in health centres,...

EACOP gave the results of the internal quarterly PIIM routine survey conducted in October by the Community Relationship Supervisors and the satellite imagery report with all the main changes detected in the villages close to EACOP activities. PWG members confirmed the results of this routine survey and so far, PIIM phenomenon is well managed without any major impacts in the different hotspots.


Chongoleani peninsula was the area most affected by newcomers' arrival seeking unskilled jobs in EACOP. Thanks to a good collaboration between EACOP site teams, contractors and communities and a clear explanation and a proper implementation of the recruitment process with a priority for the recruitment of the affected communities' members, 95% of newcomers decided to leave the area and to go back home. Changes are expected around Kakongwa road where all trucks transporting the pipelines are going to go by. Drivers will stop for a while in different dedicated parkings and this will certainly attract newcomers with different new business (food, beverages, bars, commercial sex...).

The PWG members also confirmed the quality of the EACOP stakeholder engagement (direct or via contractors) with the affected communities: they have a good information on all EACOP procedures, especially on recruitment process for unskilled/semi-skilled and skilled jobs. This is a key information to discourage newcomers from other districts coming to seek unskilled jobs inside EACOP. Regular engagement meetings have allowed us to build trustful relationships which is important to manage properly the PIIM phenomenon and its impacts. Contractors do not start any activity before providing the communities nearby all the information regarding their scope of work, number and profile of jobs for how long and the procedures to apply for a job.

Finally, EACOP PIIM team received the first results of the PIIM campaign on radio, social media and newspapers: the PWG members were very positive and asked EACOP some material to use in their own meetings which was accepted by EACOP. The campaign is focused on fraudulent advertisements, job categories (unskilled, semi-skilled and skilled) and the recruitment process applied by EACOP Contractors for each jobs category. The general audience has well understood the meaning of our messages qualified as clear and without any ambiguity.

This campaign will last until April 2024.

## Social Media Messages



## Communication Channels



**National radios:** Clouds FM, Radio Free Africa.

**Local radios:** Pangani FM (Tanga), Standard FM (Singida), CG FM (Tabora), Storm FM (Geita), Kwizera FM (Kagera), Dodoma FM (Dodoma), Gold FM (Shinyanga), ORS FM (Manyara).

**Frequency:** Radio averts on a monthly basis /once a week.



**YouTube:** one video teaser post once a quarter.

**LinkedIn:** 4 posts per month.

**Facebook**

**Twitter:** 5 posts per week in a month / once per quarter.

**Instagram:** 4 posts per week in a month / once per quarter.



**Swahili Newspaper:** Mwananchi - 2 feature articles each month.

**English Newspaper:** The Guardian - 2 feature articles each month.

EACOP website.





# REGULATORY COMPLIANCE


## Permitting in Tanzania

Continual monitoring of active sites for compliance with permitting conditions is ongoing to ensure adherence to regulatory requirements.


### Status of Permits in Tanzania as of November 2023.

S/N	Active Site	Location Area	Necessary Permits in Place
1	CY	Sojo-Nzega, Tabora	YES
2	MCPY07	Chato, Geita	YES
3	MCPY15	Handeni TC, Tanga	YES
4	PS3	Muleba, Kagera	YES
5	PS4	Mbogwe, Geita	YES
6	PS5	Igunga, Tabora	YES
7	PS6	Singida, Singida	YES
8	PRS1	Kiteto, Manyara	YES
9	PRS2	Handeni, Tanga	YES
10	MST	Tanga City, Tanzania	YES
11	Jetty	Tanga City, Tanzania	YES

## Permits Obtained per Active Locations

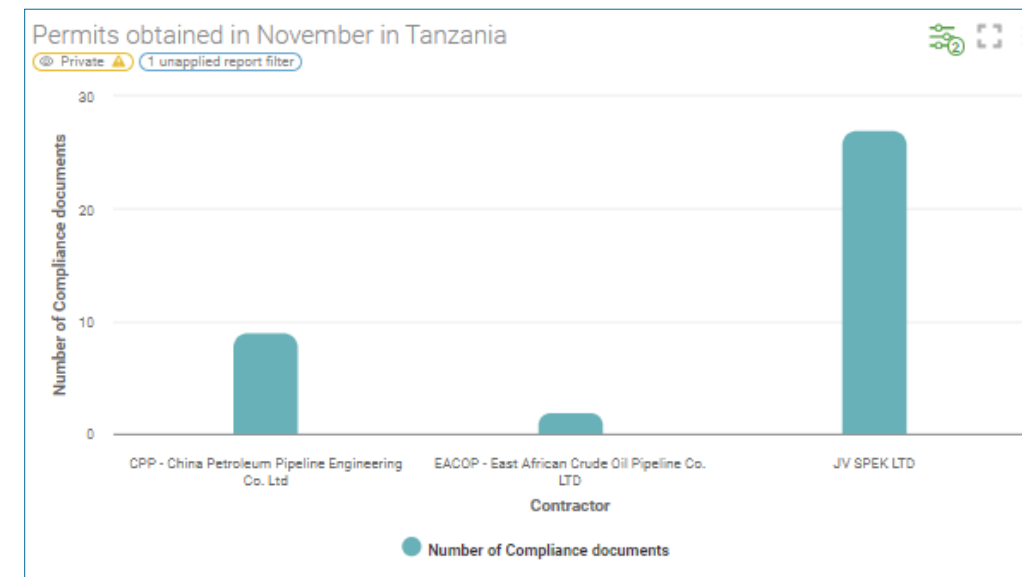

## Compliance by Project Area (Identified in the past month, includes open and closed observations)

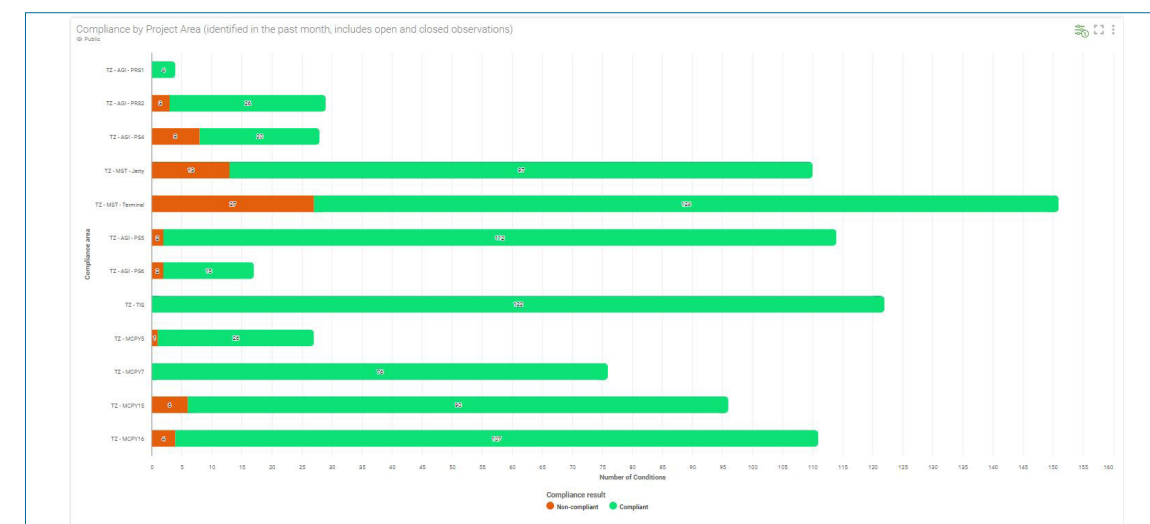

EACOP Limited has submitted an application to the Tanzania Civil Aviation Authority (TCAA) for the approval of loading arms within the Load Out Facility.

Contractors received clarification and guidance on OSHA registration and compliance certificates from EACOP Ltd. to prevent any potential obstacles in the permitting process.


Received Pre-Export Verification of Conformity (PVoC) Exemption Extension from Tanzania Bureau of Standards (TBS) and Ministry of Energy (MoE), aiding Level 1 contractors and EACOP Limited.

## Regulatory Compliance and Assurance

The site compliance spot check concluded at the coating yard, ensuring adherence to permitting conditions and maintaining compliance.



## PHOTO OF THE MONTH

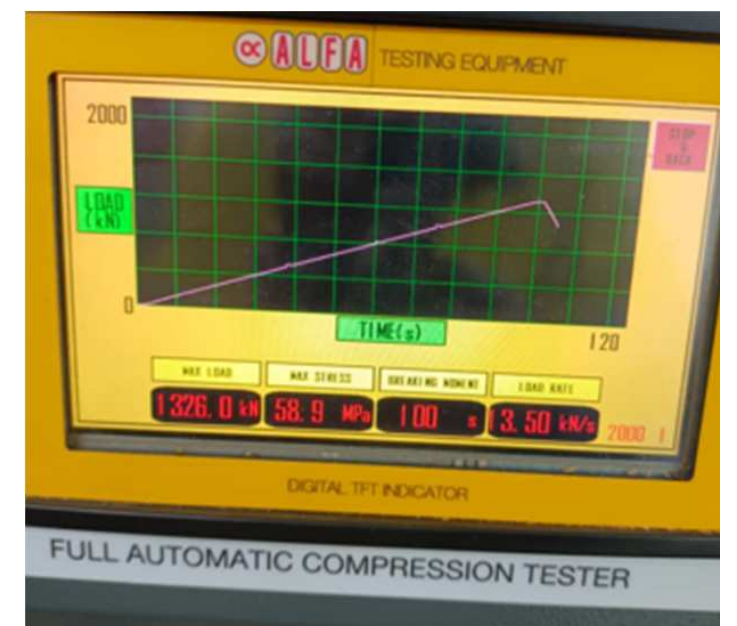

Finalizing the Trial Mix, Thermal Mock-up & Concrete Cube Test with our Floating Batching Plant.





## EAST AFRICAN CRUDE OIL PIPELINE

### **EACOP Internal Communications**

Human Resources and Corporate Affairs Department  
East African Crude Oil Pipeline (EACOP) Ltd.  
Msasani Peninsula plot no 1403, block 1, house 7.  
Brains Avenue, off chole road.  
P.O.Box. 23139, Dar es Salam, Tanzania.  
Email: [infor.tz@eacop.com](mailto:infor.tz@eacop.com)

©2023 All Rights Reserved.  
No part of this publication should be reproduced, altered in a whole or part without prior written notice from the East African Crude Oil Pipeline Management.

